

CURRENT CONSTRUCTION ACTIVITIES

LAST WEEK - WEEK ENDING 08/31/2024

Roof:

- TPO roof install @ Court room add
- Walk Mats install
- Roof drains/ ERD's @ Court room
- RTU install/tie in @ Sally Port & Court addition

3rd Floor:

- Drywall expansion joint install per (RFI 120)

2nd Floor:

- Elec device install / Perm lighting install
- Electrical room equipment install

1st Floor:

- Drywall/Insulation/ Drywall finishing
- Electrical room equipment install
- Exterior framing/sheathing @ court add
- continue hanging duct in court addition
- grills/ diffusers install
- SOMD/concrete remediation @ radius
- Elec device install / Perm lighting install
- Electrical o/h at court addition
- Fire Protection sprinkler heads
- Installing 6" o/h roof drains & ERD's piping
- Running data cable

Basement:

- Drywall/Insulation/security mesh install
- Existing elevator modernization continues / electrical rework
- Drywall finishing
- Primer/paint begins @ walls & ceilings
- Fire Protection sprinkler heads
- Concrete stairs @ basement entrance

Exterior:

- Grading for curb & gutter/site grading
- BMP rework/refresh
- Fiber cement siding install continues at West/South Elevations
- Domestic waterline tie - in
- U/G conduits/ form work/concrete for light pole bases
- Pouring sidewalks @ public retrieval & loading dock

THIS WEEK - WEEK ENDING 09/07/2024

Roof:

- Louvre install @ Existing roof
- Electrical tie in RTU's @ court addition

3rd Floor:

- Tie in FA devices to panel
- Flooring install @ bathrooms
- Wiring duct detectors allowing air to be turned on

2nd Floor:

- Cable tray install
- Framing/ drywall @ existing columns (RFI 115)
- Conduits @ RTCC for access flooring
- Electrical device install

1st Floor:

- Drywall/Insulation install
- Drywall finishing
- Electrical room equipment install
- duct sealant / insulation
- Elec device install / Perm lighting install
- Electrical o/h at court addition
- Fire Protection sprinkler heads
- Courtroom mock up
- Interior framing @ court add
- Upgraded FA panel install/ programming

Basement:

- Drywall/Insulation/security mesh install
- Existing elevator modernization continues
- Drywall finishing
- Primer/paint @ walls & ceilings
- Fire Protection sprinkler heads

Exterior:

- Pouring curb & gutter
- BMP rework/refresh
- Fiber cement siding install continues at courtyard
- U/G conduits/ form work/concrete for light pole bases
- Waterproofing (court add)
- Begin Wall B survey/grading/footings
- Side walk / site entrance demo
- Irrigation piping install
- Brick install @ court add following waterproofing
- EFIS install @ Soffits


 JOBSITE PHOTOS



Sheathing @ Corner of North & South Elevations



Light Fixture at 3rd Floor Corridor

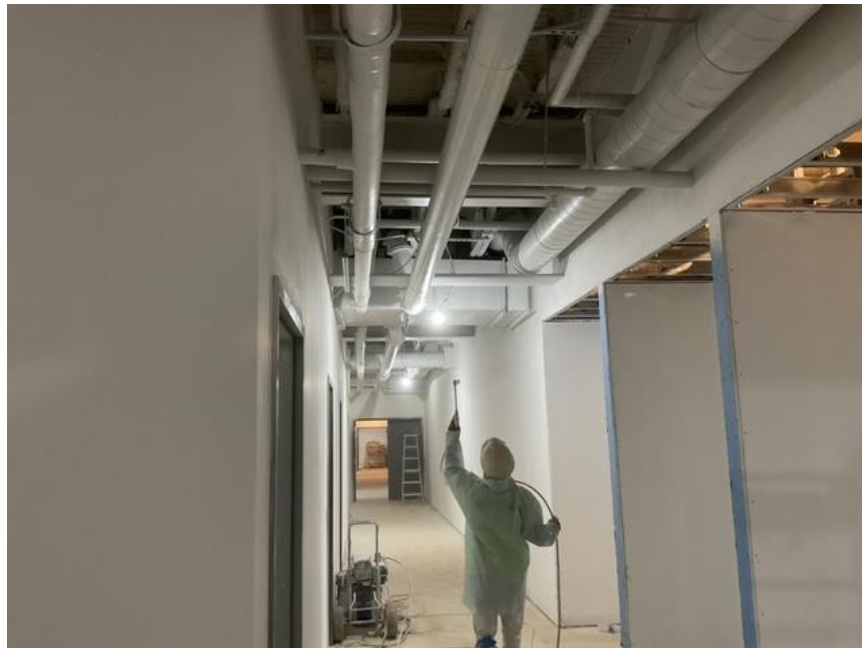















Dryfall at Corridors w/ Exposed Ceilings



RTU's @ Courts Addition

 WEATHER

Weather delays this week: 0

1  92° 68°	2  92° 71°	3  82° 62°	4  81° 65°	5  79° 65°	6  75° 64°	7  83° 61°
8  79° 58°	9  82° 57°	10  84° 58°	11  82° 61°	12  80° 62°	13  79° 62°	14  80° 61°

- Total Weather Delays: 29

SAFETY REPORT

- Days without an accident: 285
- Days without lost time: 285

MILESTONE TRACKING

- Construction Start: August 21, 2023
- Current Contract Completion Date: Mar 14, 2025
