

CURRENT CONSTRUCTION ACTIVITIES

LAST WEEK - WEEK ENDING 09/14/2024

Roof:

- Condensing Unit Tie in
- Power to RTU's @ Court & Sally Port roof

3rd Floor:

- Tile Install @ Bathrooms
- Filling existing floor cores (floor prep)
- Installing LV cable for cameras & doors (G,C, & E)
- Coring holes for electrical floor boxes
- Install HMD at roof access

2nd Floor:

- Cable Tray install/ pulling cable
- Installing permanent lighting @ grid
- Filling existing floor cores (floor prep)
- Temp power to smoke dampers (air start up)
- Installing HMD at roof access (court & Sally Port)
- Glass Install (RFI 119)

1st Floor:

- Drywall/Insulation/ Drywall finishing
- Electrical room equipment install
- continue hanging duct in court addition
- grills/ diffusers install
- Elec device install / Perm lighting install
- Electrical o/h & in-wall at court addition
- In wall LV r/l for thermostats
- Fire Protection installation
- In wall & o/h plumbing r/i
- framing and drywall around existing columns per RFI 115
- installing drywall expansion joints per RFI 120
- installing HMD & hardware

- installing air transfers @ Sally Port
- temp doors & coverings for air start up
- mounting bracket install for counter tops @ interview rooms

Basement:

- Drywall/Insulation/security mesh install
- Grid install
- Existing elevator modernization continues
- Drywall finishing
- Primer/paint walls, ceilings, doors/frames (Sally Port)
- Fire Protection installation
- Installing HMD & hardware
- Temp doors & covering for air start up
- Permanent lighting install

Exterior:

- Grading for curb & gutter/site grading
- Curb & gutter form/pour
- Fiber cement siding install continues at West/South Elevations
- U/G conduits/ form work/concrete for light pole bases
- EFIS install @ Soffits @ basement entrance
- Brick install @ court addition
- Rework/reinstall storm MH's/ sidewalks at site entrance
- Waterproofing at court addition

THIS WEEK - WEEK ENDING 09/07/2024

Roof:

- Condensing Unit Tie in
- Power to RTU's @ Court & Sally Port roof

3rd Floor:

- Tile Install @ Bathrooms
- Drop tile install

2nd Floor:

- Cable tray install
- Tile Install @ Bathrooms
- Drop tile install

1st Floor:

- Drywall/Insulation/ Drywall finishing
- continue hanging duct in court addition
- grills/ diffusers install
- Elec device install / Perm lighting install
- Electrical o/h & in-wall at court addition
- In wall LV r/i for thermostats
- Fire Protection installation
- In wall & o/h plumbing r/i
- Hardware install @ HMD

Basement:

- Drywall/Insulation/security mesh install
- Grid install
- Existing elevator modernization continues
- Primer/paint walls, ceilings, doors/frames (Sally Port)
- Fire Protection installation
- Installing hardware @ HMD
- Permanent lighting install
- New elevator install

Exterior:

- Grading for curb & gutter/site grading
- Fiber cement siding install continues at West/South Elevations
- U/G conduits/ form work/concrete for light pole bases
- EFIS install @ Soffits @ courtyard entrance
- Brick install @ court addition
- Rework/reinstall storm MH's for PEMB
- GA Power on site for EV Charger trenching

 JOBSITE PHOTOS




Brick at Radius Corners



Siding at Courtyard





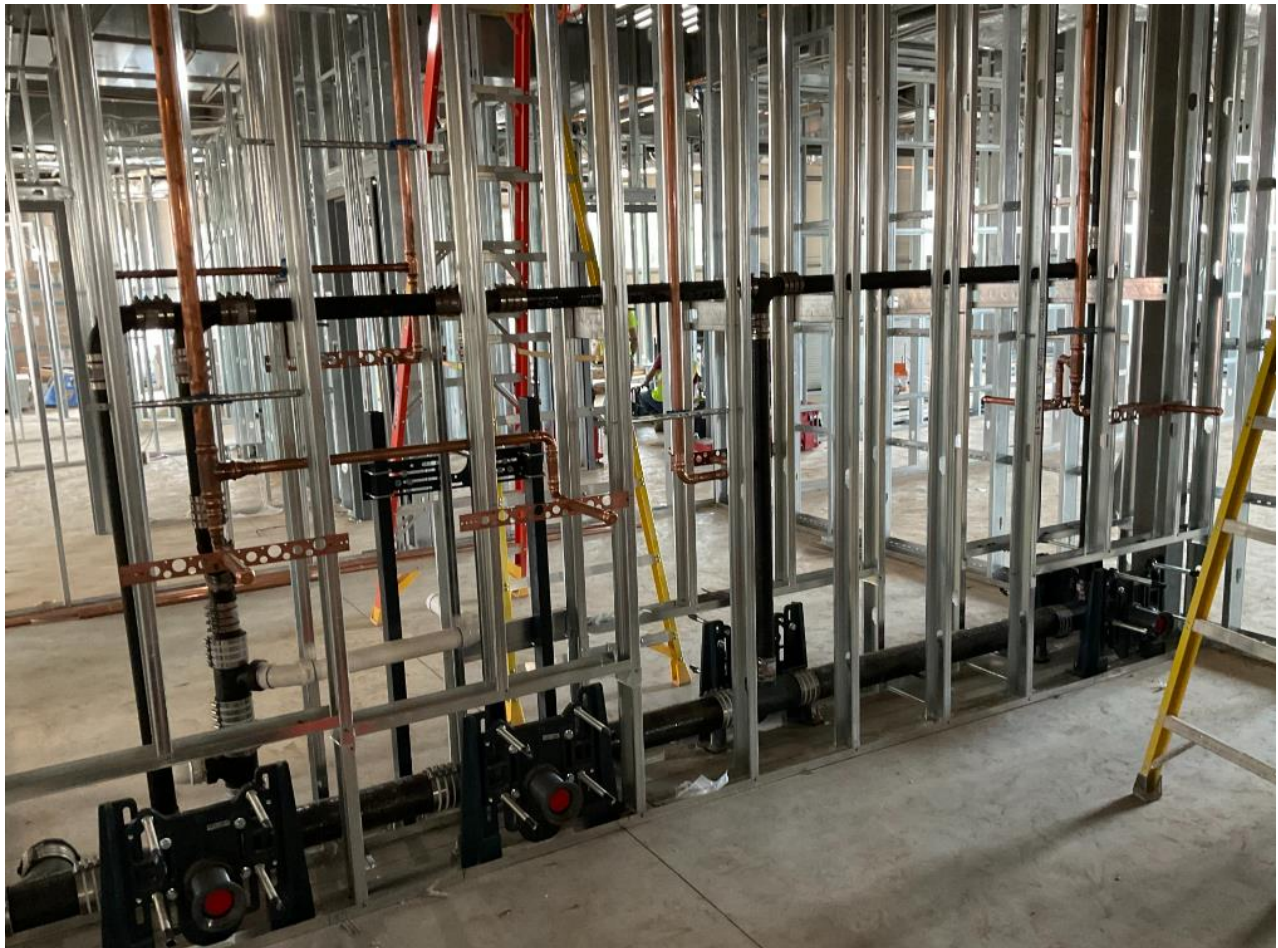











Tile at Restrooms



Framing & MEP Rough-In at Courts Addition Restrooms

 WEATHER

Weather delays this week: 0

8  81° 61°	9  85° 60°	10  85° 63°	11  80° 63°	12  71° 63°	13  74° 66°	14  73° 68°
15  79° 66°	16  81° 60°	17  78° 62°	18  81° 64°	19  85° 64°	20  87° 65°	21  86° 65°

- Total Weather Delays: 29

SAFETY REPORT

- Days without an accident: 295
- Days without lost time: 295

MILESTONE TRACKING

- Construction Start: August 21, 2023
- Current Contract Completion Date: Mar 14, 2025
