

CURRENT CONSTRUCTION ACTIVITIES

LAST WEEK - WEEK ENDING 10/5/2024

Roof:

- Louver installation
- RTU gas lines

3rd Floor:

- Tile Install @ Bathrooms
- Carpet / LVP install
- Drop tile install
- Hanging/finishing hard ceilings
- Installing fixtures in bathrooms
- Elec/LV device install
- Permanent linear lighting in bathrooms

2nd Floor:

- LV cable install
- Tile Install @ Bathrooms
- Air testing FP lines
- Drop tile install
- Hanging/finishing hard ceilings
- Elec device install
- Permanent linear lighting in bathrooms

1st Floor:

- Drywall/Insulation/ Drywall finishing
- Electrical o/h & in-wall at court addition
- Fire Protection installation
- Tile install @ bathrooms
- Store front install @ radius & court addition

- Cable tray install
- Pony wall/detention stool steel install

Basement:

- Grid install
- Grill/ diffuser install
- Existing elevator modernization continues

- Primer/paint walls, doors/frames
- Fire Protection installation
- Permanent lighting install
- New elevator install
- Tile install @ bathrooms
- Electrical rooms / transformers/panels/terminations

Exterior:

- Grading for curb & gutter/site grading
- Fiber cement siding install continues at West/South Elevations
- U/G conduits/concrete for light pole bases
- EFIS install @ Soffits @ courtyard entrance
- GA Power on site for EV Charger trenching
- Curb & gutter form/pour
- Form/pour sidewalks
- Grading for PEMB
- Backer rod & caulking @ brick control joints
- ACM panel installation @ main entrance
- Stair install @ SP
- Irrigation line installl

THIS WEEK - WEEK ENDING 10/12/2024

Roof:

- Louver installation @ court roof
- RTU gas lines
- Court roof rework (rfi 128)

3rd Floor:

- Carpet / LVP install
- Drop tile install
- Hanging/finishing hard ceilings
- Installing fixtures in bathrooms
- Final paint

2nd Floor:

Drop tile install

- Hanging/finishing hard ceilings
- Elec device install
- Permanent linear lighting in bathrooms
- LV cable install

1st Floor:

- Drywall/Insulation/ Drywall finishing
- Electrical in-wall at court addition
- Elec device install
- Fire Protection installation
- Tile install @ bathrooms
- Glass install @ court addition
- Cable tray install
- Stair 1 paint

Basement:

- Existing elevator modernization continues
- Primer/paint walls, doors/frames
- Fire Protection installation
- Permanent lighting install
- Tile install @ bathrooms
- Electrical rooms / transformers/panels/terminations


Exterior:

- Site grading
- Fiber cement siding install finishes
- U/G conduits/concrete for light pole bases/ card readers
- U/G conduits from building to generator pad area
- GA Power on site for EV Charger trenching
- Form/pour sidewalks
- Grading for PEMB
- Backer rod & caulking @ brick control joints
- ACM panel installation @ main entrance
- Wall B ramps excavation/ F/R/P
- Seat walls survey/ F/R/P footings

 JOBSITE PHOTOS



Roof Screen Install at Low Roof

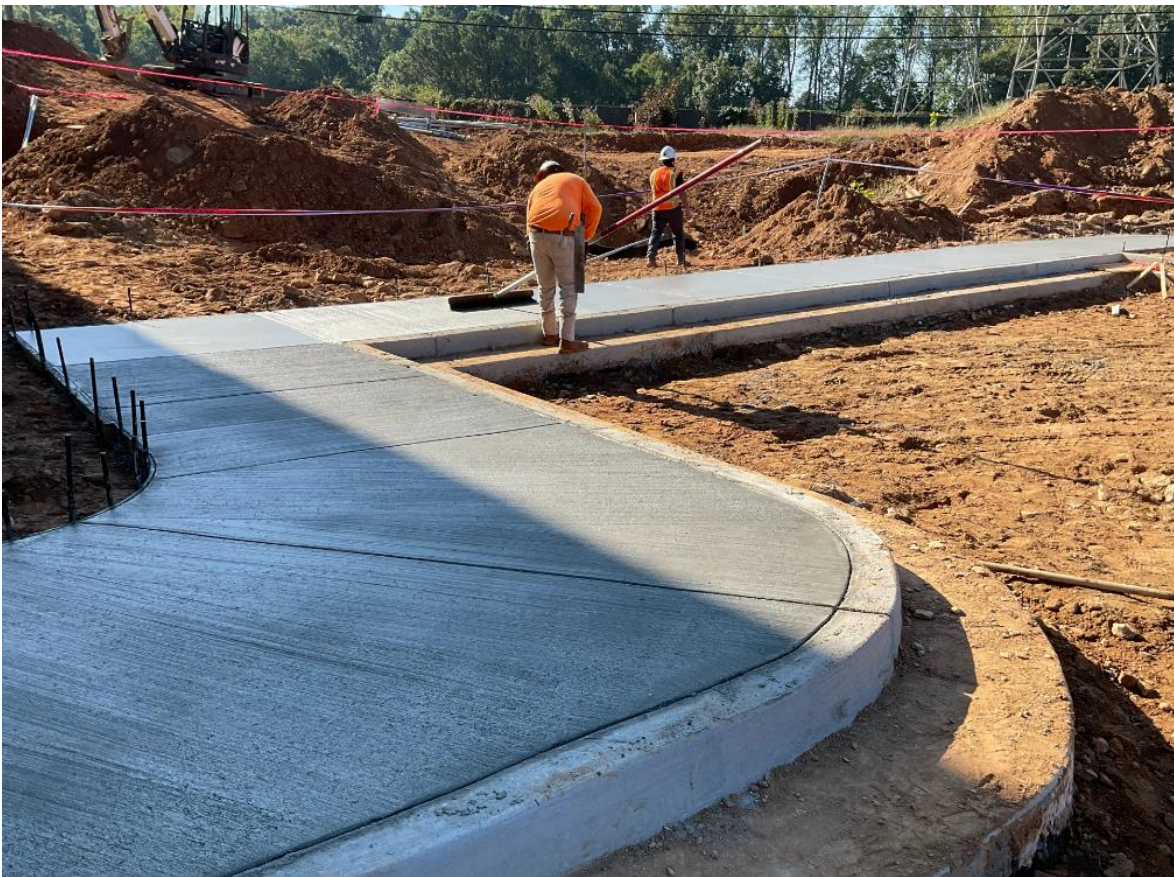

Finishing Sidewalk near Sallyport

















Storefront Install at Police Public Lobby



Grading at Parking Lot

WEATHER

Weather delays this week: 0

| | | | | | | |
|---|---|--|--|---|---|---|
| 29  79° 62° | 30  79° 63° | 1  82° 62° | 2  85° 62° | 3  85° 67° | 4  80° 63° | 5  85° 62° |
| 6  85° 62° | 7  86° 57° | 8  79° 57° | 9  79° 55° | 10  77° 49° | 11  74° 48° | 12  79° 51° |

- Total Weather Delays: 37

SAFETY REPORT

- Days without an accident: 310
- Days without lost time: 310

MILESTONE TRACKING

- Construction Start: August 21, 2023
- Current Contract Completion Date: Mar 14, 2025
