

# + CURRENT CONSTRUCTION ACTIVITIES

## LAST WEEK - WEEK ENDING 11/16/2024

### 3<sup>rd</sup> Floor:

- Touching Up Exposed Ceilings & Restrooms
- Wall Tile

### 2<sup>nd</sup> Floor:

- Pulling Cable
- Water Fountains
- Grilles at RTCC

### 1<sup>st</sup> Floor:

- Prime & Paint @ Courts
- Tile at Restrooms
- Electrical Rough-In
- Flex Lines & Slot Diffusers at Courts

### Basement:

- Light Fixtures

### Exterior:

- Metal Panels @ Courts Entrance
- Brick @ Seat Walls
- Prep and Pour Wall B Ramp Footings
- Misc. Site Grading
- Irrigation Lines

## THIS WEEK - WEEK ENDING 11/23/2024

### Roof:

- Tie-In Condensing Units at Courts Roof
- Finish TPO work per RFI 139

### 3<sup>rd</sup> Floor:

- Running Speaker Cable

### 2<sup>nd</sup> Floor:

- Fire Caulking
- Terminations at Electrical Rooms

### 1<sup>st</sup> Floor:

- Prime & Paint @ Stairs
- Cable Tray & Cable
- Sprinkler Heads
- Restroom Tile
- Toilet / Urinal Carriers
- Framing at Judges Platform
- Framing and Hanging Hard Ceilings
- Flex Lines & Slot Diffusers

### Basement:

- Cable Tray & Cable
- Wall Tile behind Water Fountains
- Water Heaters

### Exterior:

- Metal Panels @ Courts Entrance
- Chipping Rock for Ga Power
- Running Conduits to Generator
- Pouring Ramp B Walls
- Misc Site Grading
- Topsoil / Mulch at Islands


 JOBSITE PHOTOS



Roof Ladder



Ramp behind Judges Platform

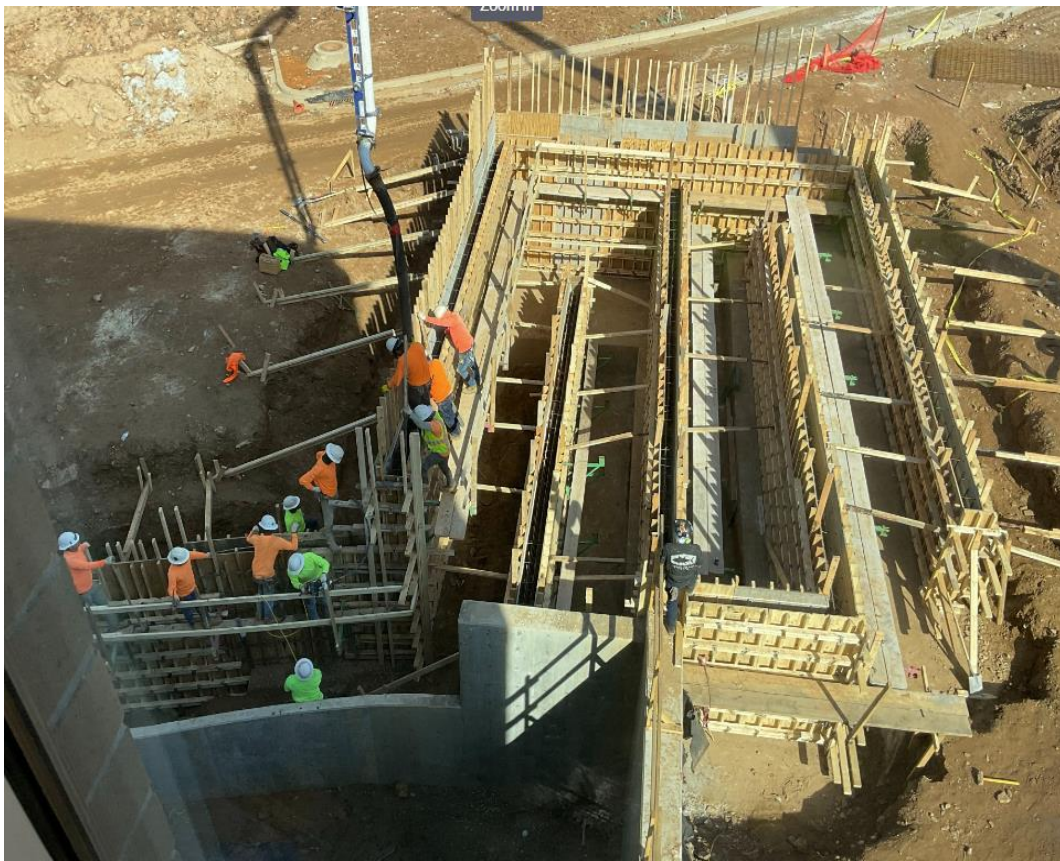















Formwork for Wall B Walls



Topsoil / Mulch at Islands

 WEATHER

Weather delays this week: 1

10  58° 54°	11  71° 49°	12  76° 49°	13  63° 44°	14  50° 45°	15  66° 39°	16  70° 42°
17  72° 45°	18  75° 55°	19  61° 59°	20  70° 38°	21  55° 35°	22  48° 35°	23  54° 34°

- Total Weather Delays: 38

## SAFETY REPORT

- Days without an accident: 335
- Days without lost time: 335

## MILESTONE TRACKING

- Construction Start: August 21, 2023
- Current Contract Completion Date: Mar 14, 2025
