CURRENT CONSTRUCTION ACTIVITIES

LAST WEEK - WEEK ENDING 01/04/2025

3rd Floor:

• Drywall Touch Up

2nd Floor:

- Drywall Touch Up
- Carpet

1st Floor:

- Pulling Data Cable
- Finishing Hard Ceilings
- Hardware for Storefront Doors

Basement:

- Installing & Finishing Drywall
- Pulling Fire Alarm Cable
- Light Fixtures
- Conduits for Low Voltage
- Fire Alarm Devices
- Sealed Concrete at Sallyport

Exterior:

- Stucco @ Retaining Wall Ramps
- Erection of PEMB
- Cast Stone Tops @ Seat Walls
- GAB for Parking Lot

THIS WEEK - WEEK ENDING 01/11/2025

3rd Floor:

Final Paint

2nd Floor:

- Wood Doors & Hardware
- Drywall Touch Up
- Electrical Work at Detention Elevator

1st Floor:

- Fire Alarm Devices
- Dropping Ceiling Tiles
- Light Fixtures
- Toilets

Basement:

- Light Fixtures
- Pulling Fire Alarm Cable
- Storefront at Data Center
- Sealed Concrete at Armory & Ammunition Areas

Exterior:

- Pour the Foundation for the Building Monument Sign
- Pour Bio Cell Walls
- Stucco at Retaining Wall
- Start-Up RTU's at Low Roof

Garage PEMB:

- Interior & Exterior Metal Wall Panels
- Electrical Rough-In

Weekly Report #61

January 7, 2025,

★ JOBSITE PHOTOS




PEMB Garage




Weekly Report #61

January 7, 2025,

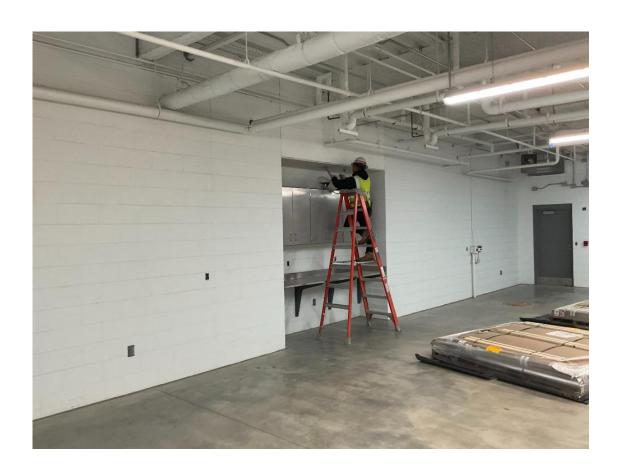

Sealed Concrete & Stainless Steel Countertops at Sallyport

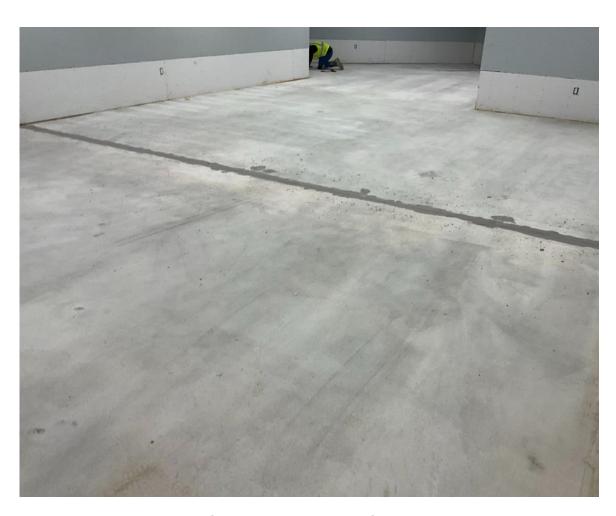

Flooring Prep Work



Weekly Report #61

January 7, 2025,



Foundation for Bio Cell



Weather delays this week: 2

29	30	31	1	2	3	4
	:		:	:	:	*
62°	65°	71°	49°	51°	52°	46°
41°	46°	39°	28°	32°	29°	29°
5	6	7 O	8 0	9 O	10 O	11
<u>,,,,</u>	***	`	`	:	21	Č
53°	46°	44°	41°	43°	34°	36°
40°	26°	24°	21°	27°	29°	21°

• Total Weather Delays: 40

July 24, 2024 Page 7

Weekly Report #61

January 7, 2025,

SAFETY REPORT

• Days without an accident: 360

• Days without lost time: 360

★ MILESTONE TRACKING

• Construction Start: August 21, 2023

• Current Contract Completion Date: Mar 14, 2025

 July 24, 2024
 Page 8
