

CURRENT CONSTRUCTION ACTIVITIES

LAST WEEK - WEEK ENDING 01/11/2025

3rd Floor:

- Final Paint

2nd Floor:

- Wood Doors & Hardware
- Drywall Touch Up
- Electrical Work at Detention Elevator

1st Floor:

- Fire Alarm Devices
- Dropping Ceiling Tiles
- Light Fixtures
- Toilets

Basement:

- Light Fixtures
- Pulling Fire Alarm Cable
- Storefront at Data Center
- Sealed Concrete at Armory & Ammunition Areas

Exterior:

- Pour the Foundation for the Building Monument Sign
- Pour Bio Cell Walls
- Stucco at Retaining Wall
- Start-Up RTU's at Low Roof

Garage PEMB:

- Interior & Exterior Metal Wall Panels
- Electrical Rough-In

THIS WEEK - WEEK ENDING 01/18/2025

3rd Floor:

- Final Paint
- Rough Cleaning

2nd Floor:

- Paint Touch Up

1st Floor:

- Dropping Ceiling Tiles
- Drywall Touch Up
- Plumbing Fixtures

Basement:

- Pulling Data & Fire Alarm Cable
- Sealed Concrete at Evidence Repository

Exterior:

- CMU & Brick for Building Monument Sign
- Grade at Bio Cell
- Prep for Heavy Duty Concrete Pour by Loading Dock

 JOBSITE PHOTOS




Prepping for Heavy Duty Concrete



Excavating at Bio Cell





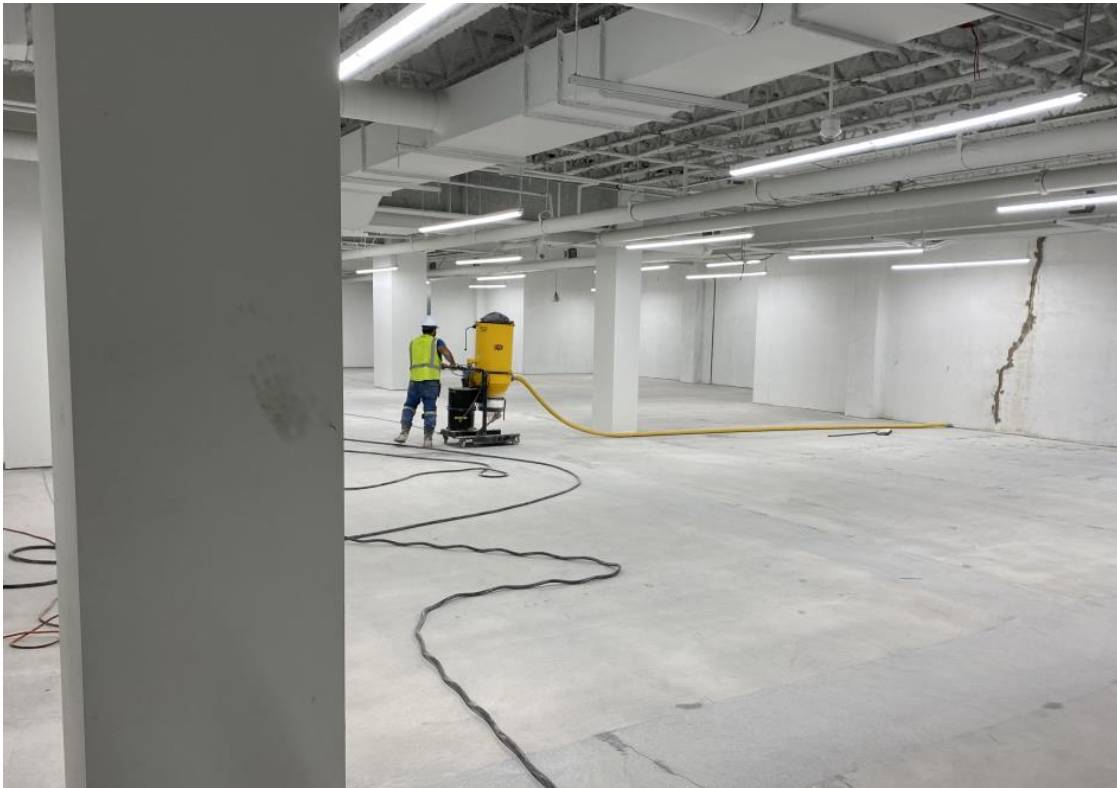











Block at Monument Sign



Sealing Concrete at Evidence Repository

WEATHER

Weather delays this week: 5

5  53° 40°	6  46° 26°	7  43° 22°	8  38° 20°	9  44° 29°	10  33° 30°	11  33° 21°
12  43° 29°	13  55° 29°	14  -- 29°	15  50° 28°	16  55° 29°	17  57° 40°	18  54° 44°

- Total Weather Delays: 45

SAFETY REPORT

- Days without an accident: 365
- Days without lost time: 365

MILESTONE TRACKING

- Construction Start: August 21, 2023
- Current Contract Completion Date: Mar 14, 2025
