

+ CURRENT CONSTRUCTION ACTIVITIES

LAST WEEK - WEEK ENDING 01/18/2025

3rd Floor:

- Final Paint
- Rough Cleaning
- Ceiling Baffles at Breakroom

2nd Floor:

- Paint Touch Up

1st Floor:

- Dropping Ceiling Tiles
- Drywall Touch Up
- Plumbing Fixtures

Basement:

- Pulling Data & Fire Alarm Cable
- Sealed Concrete at Evidence Repository

Exterior:

- CMU & Brick for Building Monument Sign
- Grade at Bio Cell
- Prep for Heavy Duty Concrete Pour by Loading Dock

THIS WEEK - WEEK ENDING 01/25/2025

3rd Floor:

- Terminate Data in the IT Room
- Labeling Electrical Devices
- Sealed Concrete

2nd Floor:

- Final Paint
- Labeling Electrical Devices
- Cutting out & Setting Floor Boxes at Raised Flooring in RTCC
- Sealed Concrete

1st Floor:

- Water Heater
- Floor Tile at Corridors
- Plumbing Fixtures
- Drop Ceiling Tiles


Basement:

- Pulling Data & Fire Alarm Cable

Exterior:

- Prepping & Laying Pavers Inside the Courtyard

 JOBSITE PHOTOS

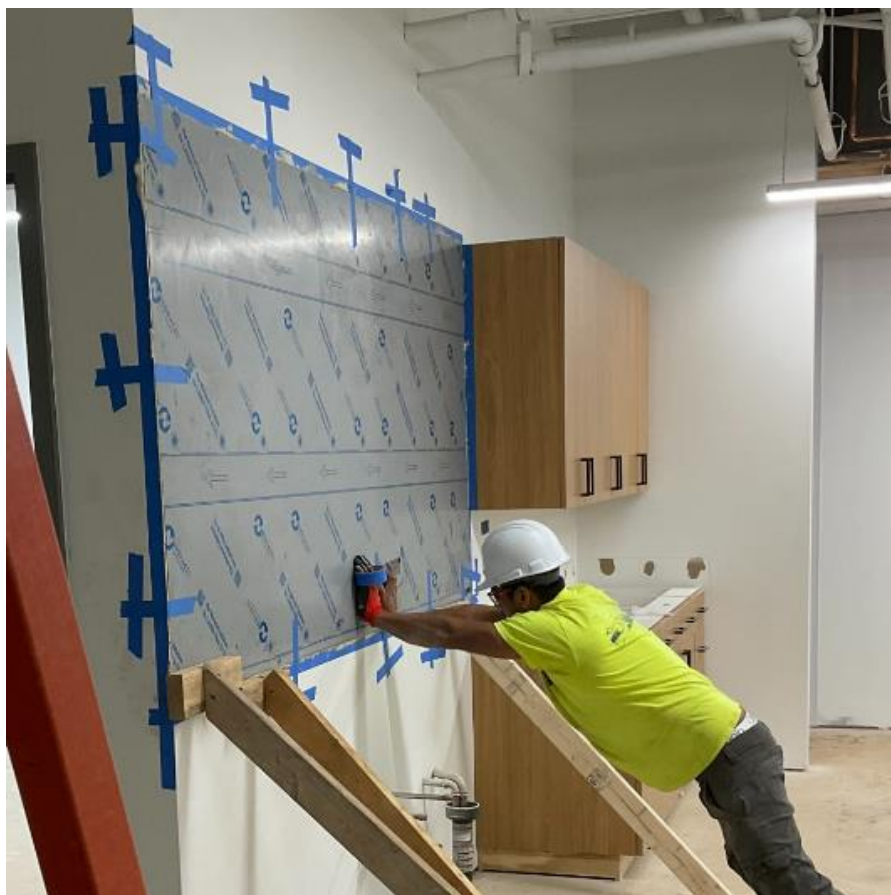

Stainless Steel Panel at Evidence Lab



Ceiling Baffles at Breakroom
















Rubber Base at 3rd Floor



Floor Tile at 1st Floor

WEATHER

Weather delays this week: 0

12  43° 29°	13  55° 29°	14  50° 32°	15  51° 27°	16  57° 32°	17  60° 40°	18  52° 44°
19  47° 16°	20  32° 17°	21  30° 14°	22  36° 19°	23  41° 23°	24  43° 21°	25  47° 29°

- Total Weather Delays: 45

SAFETY REPORT

- Days without an accident: 370
- Days without lost time: 370

MILESTONE TRACKING

- Construction Start: August 21, 2023
- Current Contract Completion Date: Mar 14, 2025
