

CURRENT CONSTRUCTION ACTIVITIES

LAST WEEK - WEEK ENDING 02/22/2025

2nd Floor:

- Architectural Punch Work
- Terminating Data Cable in the IT Room

1st Floor:

- Flooring
- Millwork at Courtroom
- Paint Touch-Up
- Faux Wood Metal Panel
- Doors & Hardware

Basement:

- VESDA at Data Center

Exterior:

- Prepping & Laying Pavers at the Plaza
- Site Fencing
- Generator Start-Up

THIS WEEK - WEEK ENDING 03/01/2025

2nd Floor:

- Terminating Data Cable in the IT Room

1st Floor:

- Fabric Panels at Courtroom
- Paint Touch-Up
- Metal Panels
- Doors & Hardware
- Fire Alarm Testing

Basement:

- Flooring
- Drywall Touch Up


Exterior:

- Prepping & Laying Pavers at the Plaza
- Soil Media at Bio Cell
- Siding Return at Entrances

 JOBSITE PHOTOS



Community Room

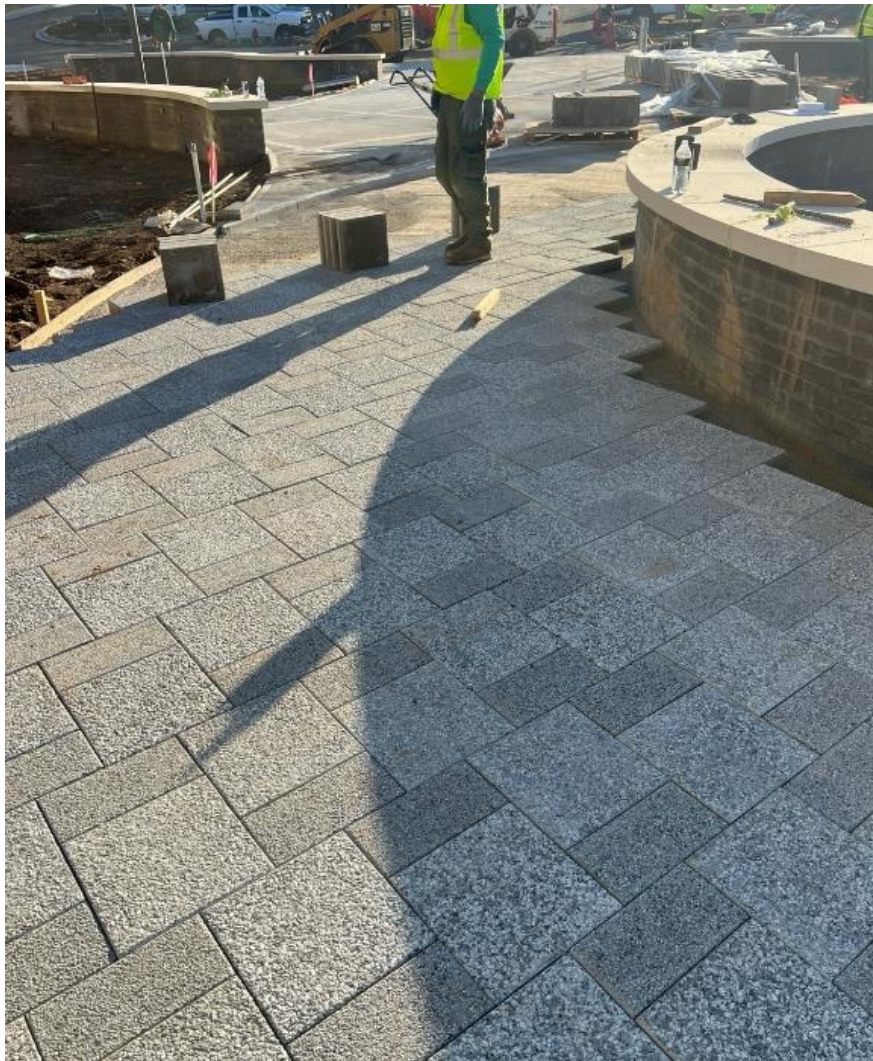

Pavers at Plaza

















Finishes at Courtroom



Metal Panels

WEATHER

Weather delays this week: 1

16  56° 28°	17  51° 28°	18  58° 39°	19  44° 25°	20  35° 18°	21  48° 24°	22  54° 29°
23  56° 35°	24  68° 39°	25  72° 40°	26  77° 48°	27  70° 39°	28  66° 42°	1  72° 38°

- Total Weather Delays: 50

SAFETY REPORT

- Days without an accident: 395
- Days without lost time: 395

MILESTONE TRACKING

- Construction Start: August 21, 2023
- Current Contract Completion Date: Mar 14, 2025
