

CURRENT CONSTRUCTION ACTIVITIES

LAST WEEK - WEEK ENDING 03/01/2025

3rd Floor:

- Furniture Install

2nd Floor:

- RTCC Equipment & Furniture Install

1st Floor:

- Final Paint
- Metal Panels
- Millwork

Basement:

- Flooring
- Millwork
- Drywall Touch Up
- Paint Touch Up
- In Row Cooling Start Up for UPS

Exterior:

- Laying Sod
- Pouring Concrete Flumes for Gates

THIS WEEK - WEEK ENDING 03/08/2025

3rd Floor:

- Furniture Install

2nd Floor:

- RTCC Equipment & Furniture Install

1st Floor:

- Final Paint
- Metal Panels


Basement:

- Flooring
- Paint Touch Up
- Existing Cab Elevator Final Inspection

Exterior:

- Laying Sod
- Pouring Concrete Flumes for Gates

 JOBSITE PHOTOS

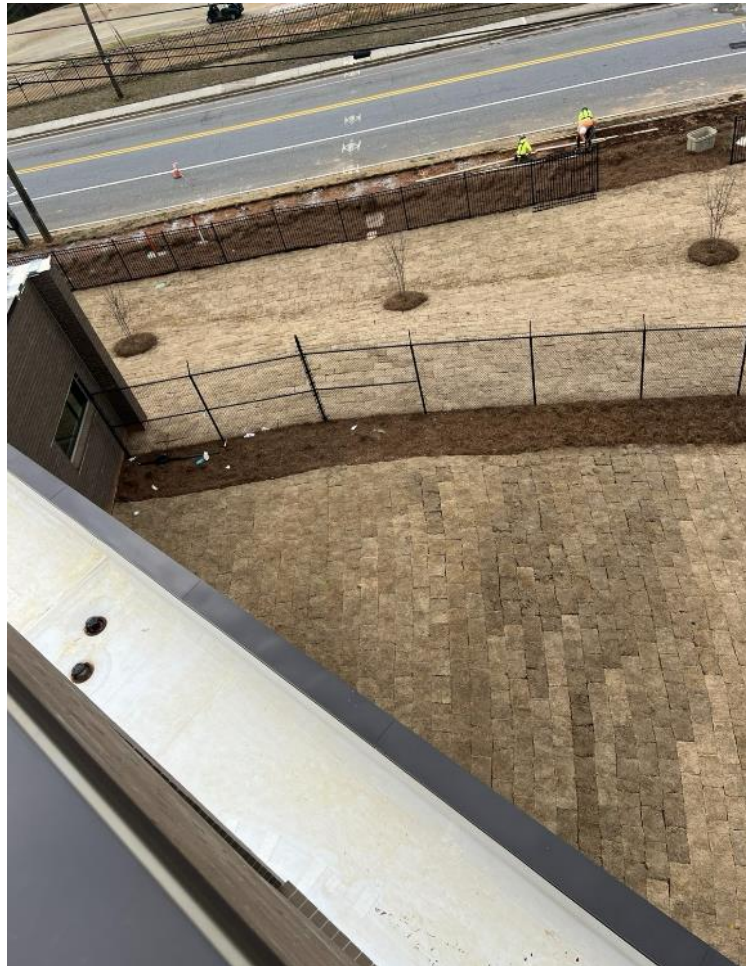

Sod



Faux Wood Panels

















Soil Media at Bio Cell



Railings at Ramps

 WEATHER

Weather delays this week: 0

2  57° 29°	3  64° 40°	4  66° 52°	5  60° 34°	6  54° 36°	7  65° 53°	8  68° 43°
9  60° 40°	10  58° 39°	11  74° 42°	12  77° 49°	13  73° 50°	14  72° 50°	15  71° 44°

- Total Weather Delays: 50

SAFETY REPORT

- Days without an accident: 400
- Days without lost time: 400

MILESTONE TRACKING

- Construction Start: August 21, 2023
- Current Contract Completion Date: Mar 14, 2025
