

CURRENT CONSTRUCTION ACTIVITIES

LAST WEEK - WEEK ENDING 03/22/2025

3rd Floor:

- Routing Data at Furniture
- Punch List Work

2nd Floor:

- Routing Data at Furniture
- Punch List Work

1st Floor:

- Terminating Data Cables at IT Closets
- Testing 1st Floor Data Cables
- Signage
- Audio Visual
- Furniture

Basement:

- Terminating Data Cables at IT Closets
- Millwork
- Final Paint
- Flooring
- Existing Elevator Inspection
- New Elevator Adjusting
- Furniture

Exterior:

- Crack & Fill at Upper Lot
- Pressure Washing Brick
- Fencing

THIS WEEK - WEEK ENDING 03/29/2025

3rd Floor:

- Routing Data at Furniture
- Punch List Work

2nd Floor:

- Routing Data at Furniture
- Punch List Work

1st Floor:

- Labeling Data Cables
- Audio Visual
- Furniture

Basement:

- Final Paint
- Flooring
- Furniture

Exterior:

- Asphalt Top Coat
- Fencing


 JOBSITE PHOTOS



Wayfinding at Basement



Fire Cabinets and AEDs at Basement

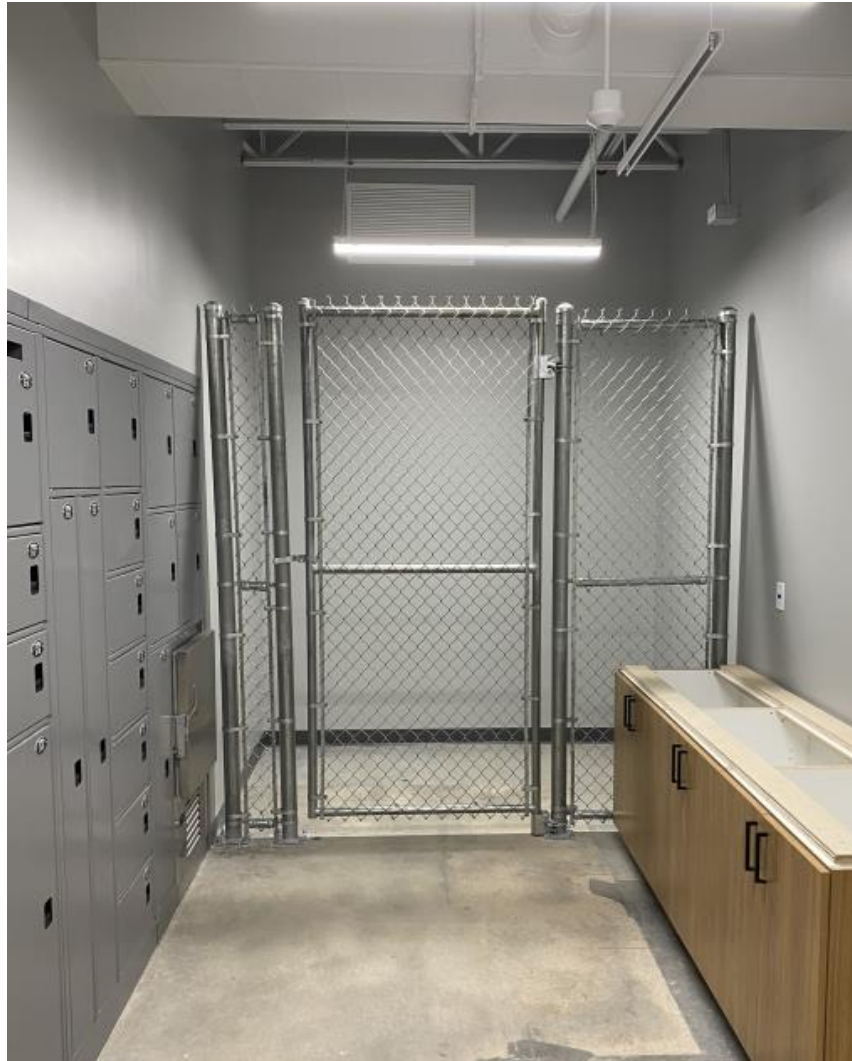















Gate at Evidence Pass Thru



Flooring at IT

WEATHER

Weather delays this week: 0

16  74° 41°	17  60° 39°	18  77° 45°	19  81° 53°	20  56° 34°	21  65° 39°	22  72° 40°
23  78° 55°	24  66° 41°	25  -- 45°	26  72° 43°	27  76° 50°	28  80° 58°	29  75° 60°

- Total Weather Delays: 55

SAFETY REPORT

- Days without an accident: 415
- Days without lost time: 415

MILESTONE TRACKING

- Construction Start: August 21, 2023
- Current Contract Completion Date: Mar 14, 2025
