Weekly Report #19

January 31st, 2024

★ CURRENT CONSTRUCTION ACTIVITIES

LAST WEEK - WEEK ENDING 01/27/2024

- Plumbing & electrical O/H & in-wall R/I Level 3
- MEP O/H R/I Level 2
- Mechanical & Electrical O/H R/I level 1
- Mechanical O/H R/I at Basement
- Existing plumbing stack line remediation
- Joist web member & beam augmentation level 1,2,3
- Continue setting geo-fabric, 57 stone, & 96" perforated CMP for 160'x21' detention pond
- Continue site utility installation
- Back fill at Sally Port foundation wall
- Main Drilling & Boring conducted test drilling at future Sanitary sewer line location 1/29-1/30 to measure depth and density of present rock
- Interior & exterior framing/sheathing
 - Interior level 2 & 3; Exterior at South elevation

THIS WEEK - WEEK ENDING 02/03/2024


- Plumbing & electrical O/H & in-wall R/I Level 3
- MEP O/H R/I Level 2
- Mechanical & Electrical O/H R/I level 1
- Mechanical O/H R/I at Basement
- Existing plumbing stack line remediation
- Joist web member & beam augmentation level 1,2,3
- Interior & exterior framing/sheathing (exterior at South/Southeast elevation & radiuses, Interior Level 2)
- Continue setting geo-fabric, 57 stone, & 96" perforated CMP for 160'x21' detention pond
- Continue site utility installation
- Back fill at Sally Port foundation wall
- Main Drilling & Boring conducted test drilling at future Sanitary sewer line location 1/29-1/30 to measure depth and density of present rock. This work was performed under Reeves Young Heavy Civil.



Weekly Report #19

January 31st, 2024

★ JOBSITE PHOTOS

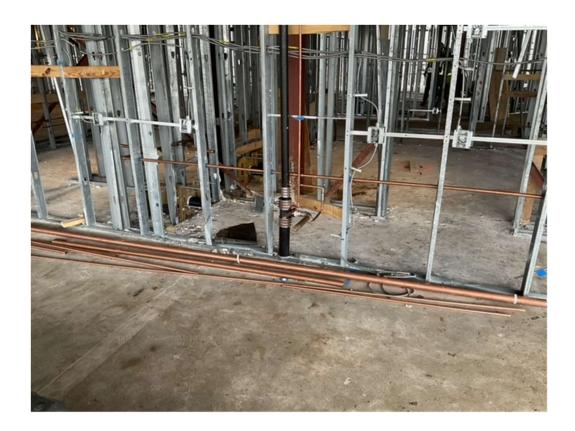

In Wall Plumbing Rough-In



Weekly Report #19

January 31st, 2024





Plumbing Rough-In



Weekly Report #19

January 31st, 2024



Fireproofing Basement



Weekly Report #19

January 31st, 2024







Mechanical Rough-In



Weekly Report #19

January 31st, 2024





Joist Web Member Augmentation



Weekly Report #19

January 31st, 2024



MD & B Test Drilling At Future Sanitary Sewery Site



Weekly Report #19

January 31st, 2024





Interior Framing



Weekly Report #19

January 31st, 2024



Exterior Framing



Weekly Report #19

January 31st, 2024





Installation Of 96" Underground Detention Pond



Weekly Report #19

January 31st, 2024





Electrical Rough-In



January 31st, 2024



Weather delays this week: 3

REEVES TOU

21	22 O	23	24	25 C	26	27
**	_	7	7			-
41°	48°	47°	56°	71°	68°	63°
25°	38°	45°	55°	58°	54°	42°
28	29 O	30	31	1 0	2	3
_	***	**	*	*	*	**
47°	54°	57°	54°	59°	64°	61°
37°	29°	38°	29°	37°	40°	42°

• SSPHQ jobsite received 2.5" of rain on 1/25/24. This caused any exterior work (exterior framing, concrete & CMU work, site work) to cease on 1/25-1/26 due to unsafe conditions. Site also received an additional 0.5" of rain over the weekend on 1/27 causing majority exterior work to not continue until 1/30 as Monday 1/29 was spent mitigating water retention

Total Weather Delays: 7

Weekly Report #19

January 31st, 2024

SAFETY REPORT

• Days without an accident: 138

• Days without lost time: 138

★ MILESTONE TRACKING

• Construction Start: August 21, 2023

• Current Contract Completion Date: Mar 14, 2025
