

CURRENT CONSTRUCTION ACTIVITIES

LAST WEEK

- Continued Structural Steel at the Second Floor
- Began Decking Second Floor
- Continued Interior and Exterior CMU Walls
- Continued MEP Interior Wall Rough-in
- Poured Steel Diamonds at the First Floor


THIS WEEK

- Continue Setting Structural Steel at Second Floor
- Prep Second Floor Metal Deck for Concrete Slab Pour
- Pour Elevated Deck Slab
- Continue MEP in-wall Rough-in
- Begin Overhead Rough-in
- Continue Interior and Exterior CMU Walls

JOBSITE PHOTOS



Elevated Slab on Deck Prep at the Second Floor

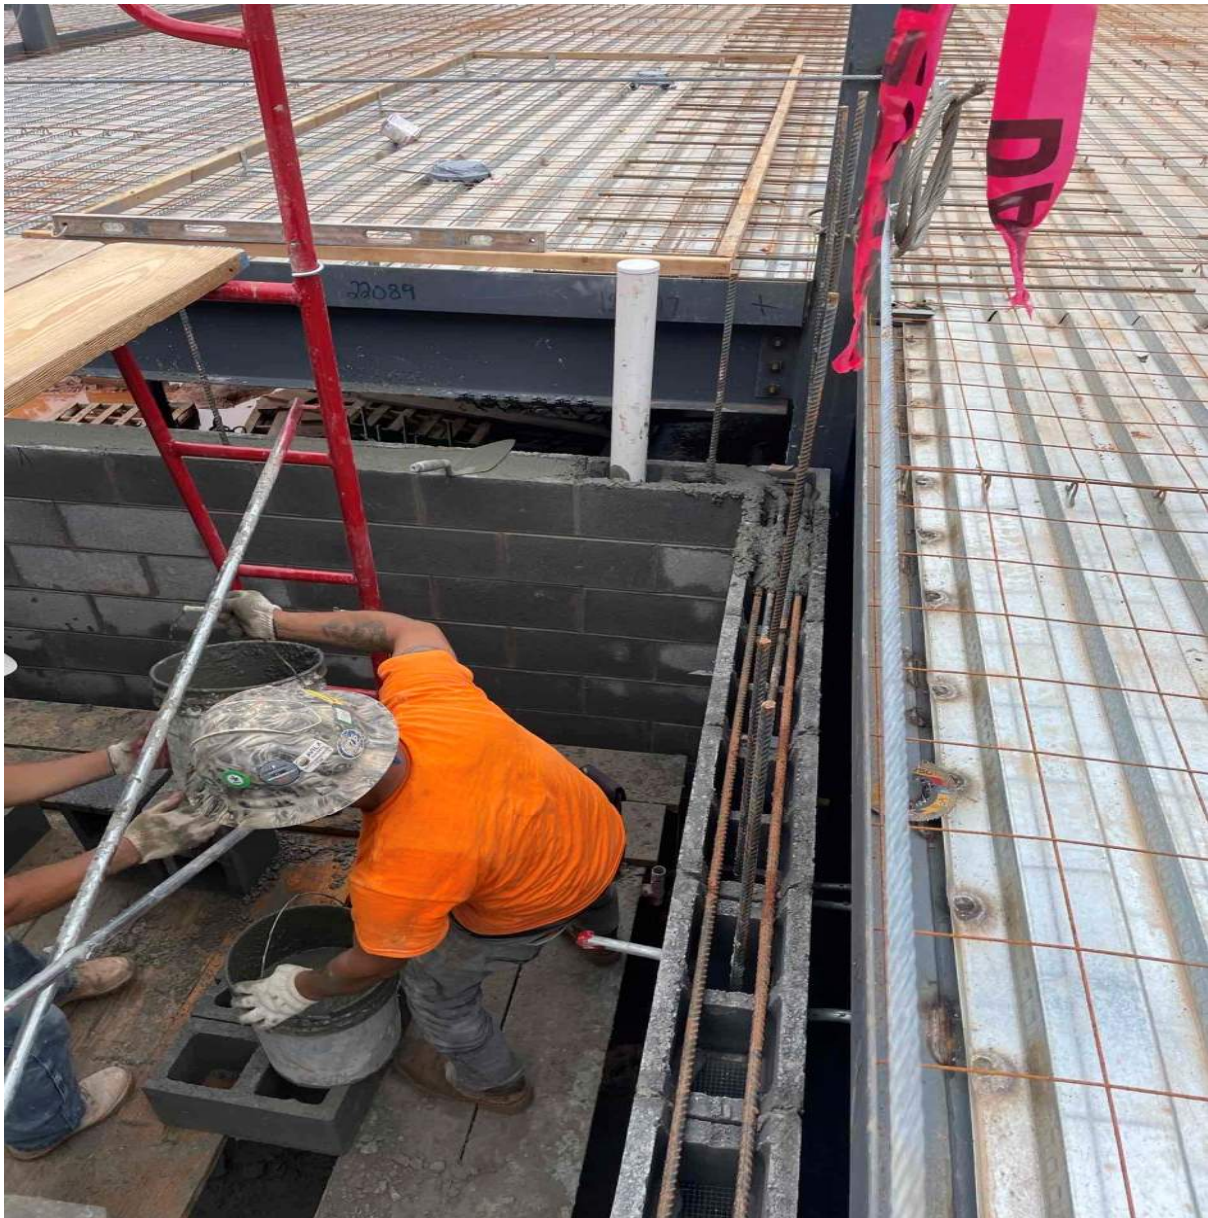

Continuing Installation of Interior CMU



Continuing in-wall Rough-in and CMU


WEATHER

Weather delays last week: 2



MANPOWER

MANPOWER GRAPH

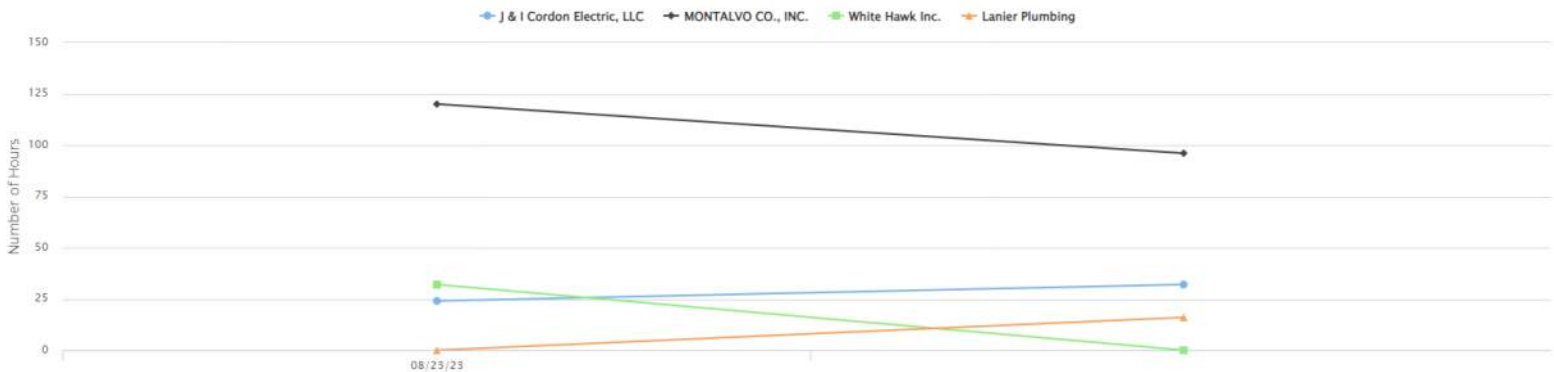

SAFETY REPORT

- Days without an accident: 97
- Days without lost time: 97

MILESTONE TRACKING

- Construction Start: April 10, 2023
- Current Contract Completion Date: June 10, 2023
