

+ CURRENT CONSTRUCTION ACTIVITIES

LAST WEEK

- Continued MEP Interior Wall Rough in
- Completed Concrete Slab on Grade Pour Floor Protection
- Completed Installation of Floor Protection at Apparatus Bay
- Continued Interior Framing on First Floor
- Completed TPO Install on Apparatus Bay Roof
- Completed Concrete Footings for Retaining Wall
- Completed Tree Removal at Mount Vernan Entrance
- Completed Out Rigger and Metal Decking Installation
- Poured Footings for Remaining Retaining Wall Near Apparatus Bay

THIS WEEK

- Begin Install of Wood Windows on First and Second Floor
- Form Walls for Retaining Wall at Spalding Rd Entrance
- Continue Interior Framing on First Floor
- Continue Shingle Roof Underlayment Installation
- Continue MEP Interior Rough in on First and Second Floor
- Continue Installation of Waterproofing at Exterior Building Sheathing

+ JOBSITE PHOTOS



Completed Concrete Slab on Grade Pour and Floor Protection




Installation of TPO Roofing at Apparatus Bay



Asphalt Roof Underlayment Installation


WEATHER

Weather delays last week: 0

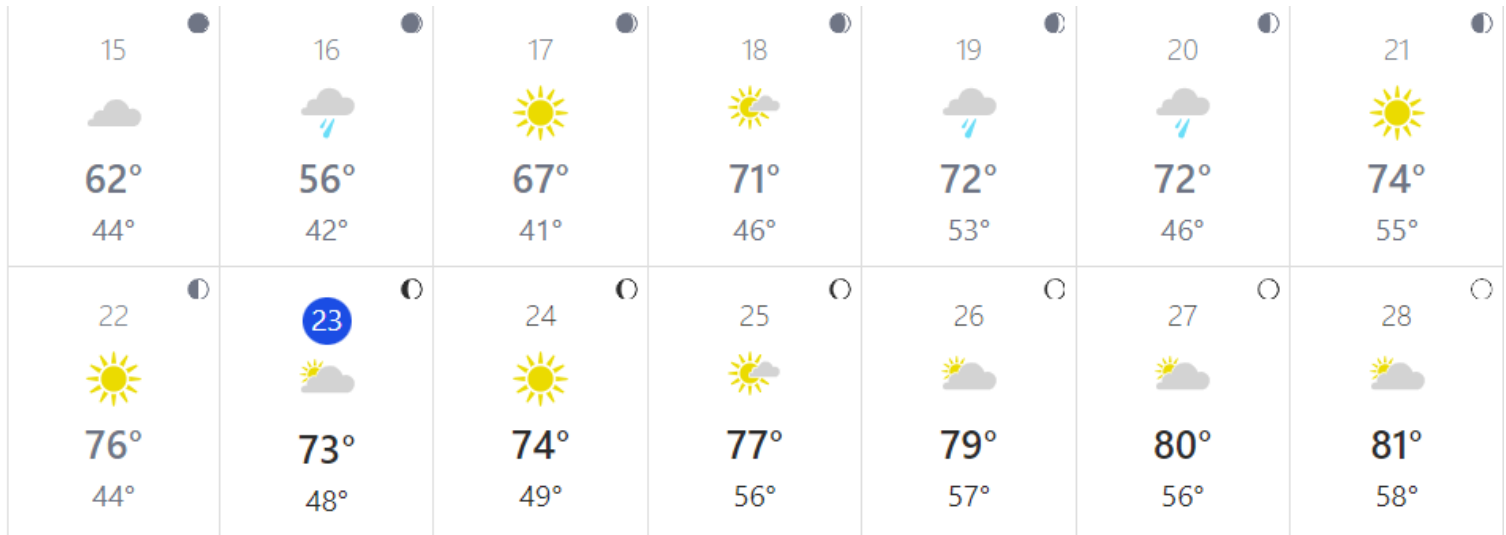

MANPOWER

MANPOWER GRAPH

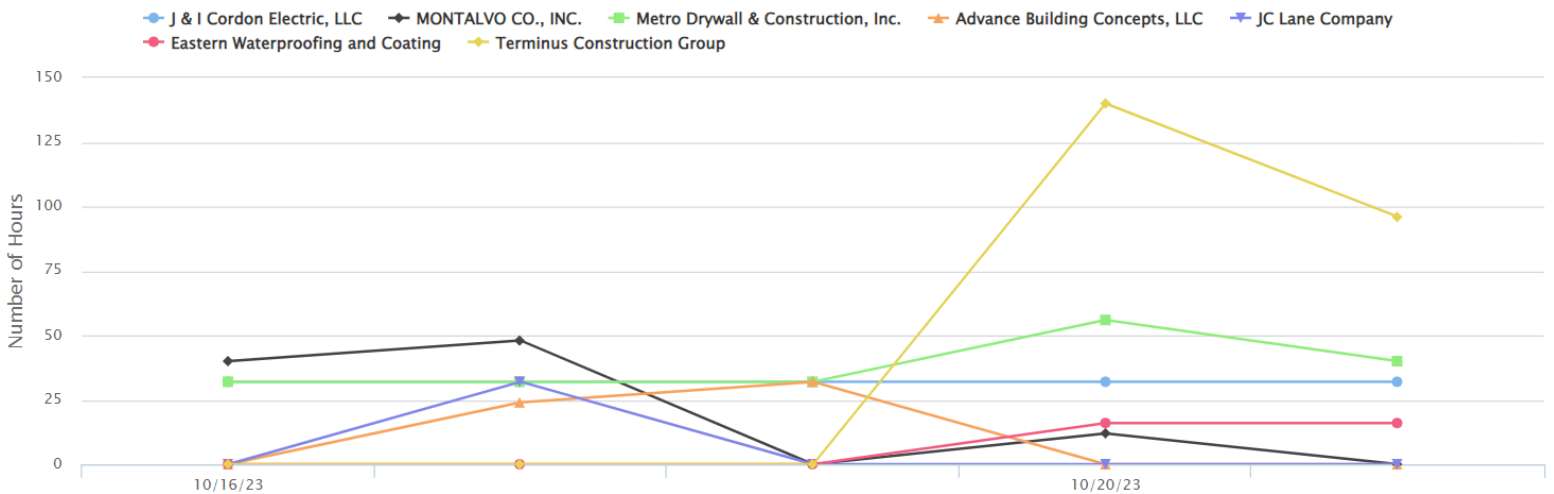

SAFETY REPORT

- Days without an accident: 140
- Days without lost time: 140

MILESTONE TRACKING

- Construction Start: April 10, 2023
- Current Contract Completion Date: June 10, 2024
