

## + CURRENT CONSTRUCTION ACTIVITIES

### LAST WEEK

---

- Completed Shingle Roofing Installation
- Continued Bifold Door Installation at Apparatus Bay
- Completed Header Curb Pour and Sleaving and Prep at Mt Vernon Parking Lot
- Continued In-Wall and Overhead MEP Installation
- Continued Brick Veneer and Cast Stone Installation on Mt Vernon Side
- Began Grading for Asphalt Parking Lot
- Began Backfilling on the east side of the building

### THIS WEEK

---

- Begin RCP Piping Installation for Storm Line
- Continue Bifold Doors Installation at Apparatus Bay
- Begin Prepping for Asphalt at Mt Vernon Parking Lot
- Continue In-Wall and Overhead MEP Installation on Second Floor
- Continue Brick Veneer and Cast Stone Installation

 JOBSITE PHOTOS



Began Grading for Asphalt Parking Lot





Began Backfilling on the east side of the building






Completed Header Curb and Sleeving and Prep at Mt Vernon Parking Lot




## WEATHER

Weather delays last week: 0

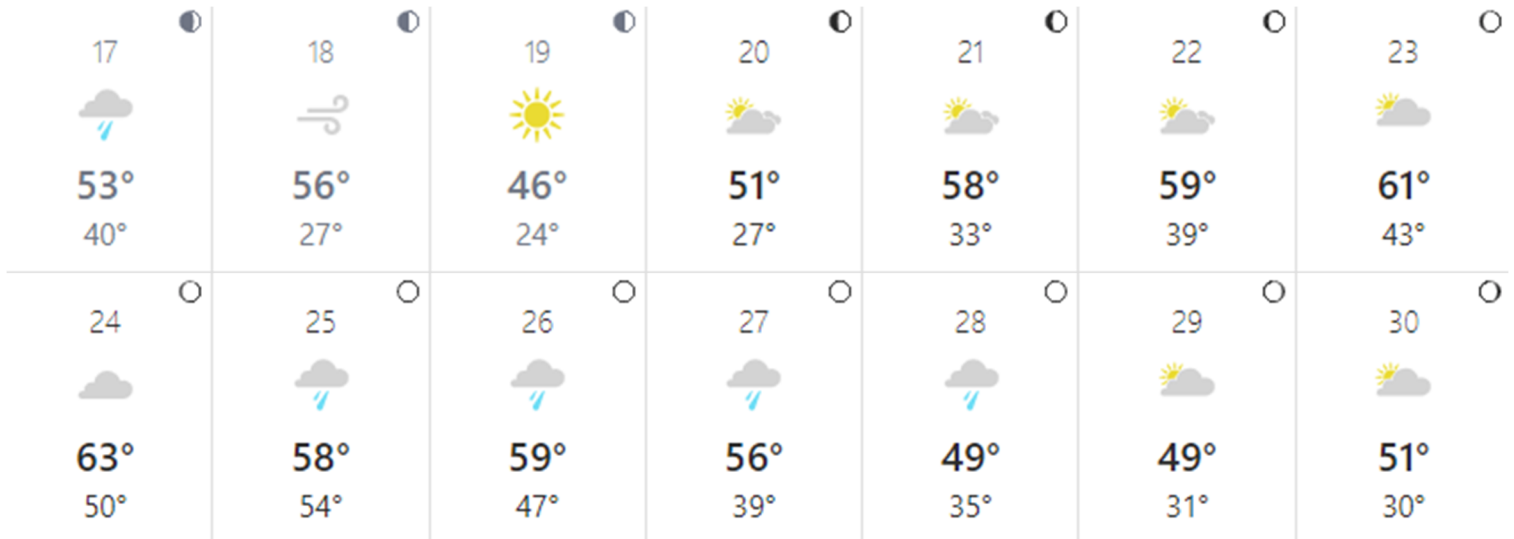

## MANPOWER

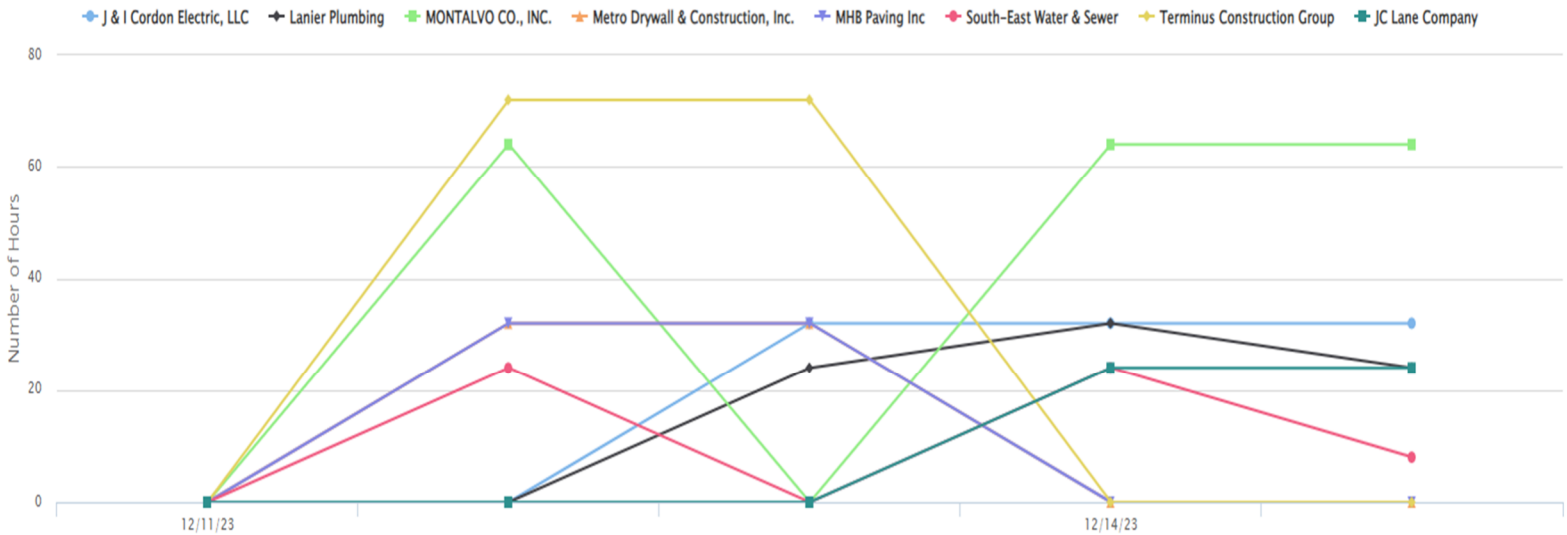

## SAFETY REPORT

- Days without an accident: 175
- Days without lost time: 175

## MILESTONE TRACKING

- Construction Start: April 10, 2023
- Current Contract Completion Date: June 10, 2024
