

## + CURRENT CONSTRUCTION ACTIVITIES

### LAST WEEK

---

- Began Installing RCP Piping for Storm Line
- Poured Asphalt Paving at Mt Vernon Entrance
- Began One-Siding and Insulation on Second Floor
- Continued In-Wall and Overhead MEP Installation
- Continued Brick Veneer and Cast Stone Installation on Mt Vernon Side
- Installed Manhole Structures for Storm Line
- Continued Backfilling and Grading on East Side of Building

### THIS WEEK

---

- Continue RCP Piping Installation for Storm Line
- Complete Bifold Doors Installation at Apparatus Bay
- Continue One-Siding and Insulation on Second Floor
- Continue In-Wall and Overhead MEP Installation on Second Floor
- Continue Brick Veneer and Cast Stone Installation

+ JOBSITE PHOTOS



Poured Asphalt Paving at Mt Vernon Entrance




Installed Manhole Structures for Storm Line




Began Installing RCP Piping for Storm Line

## WEATHER

Weather delays last week: 0

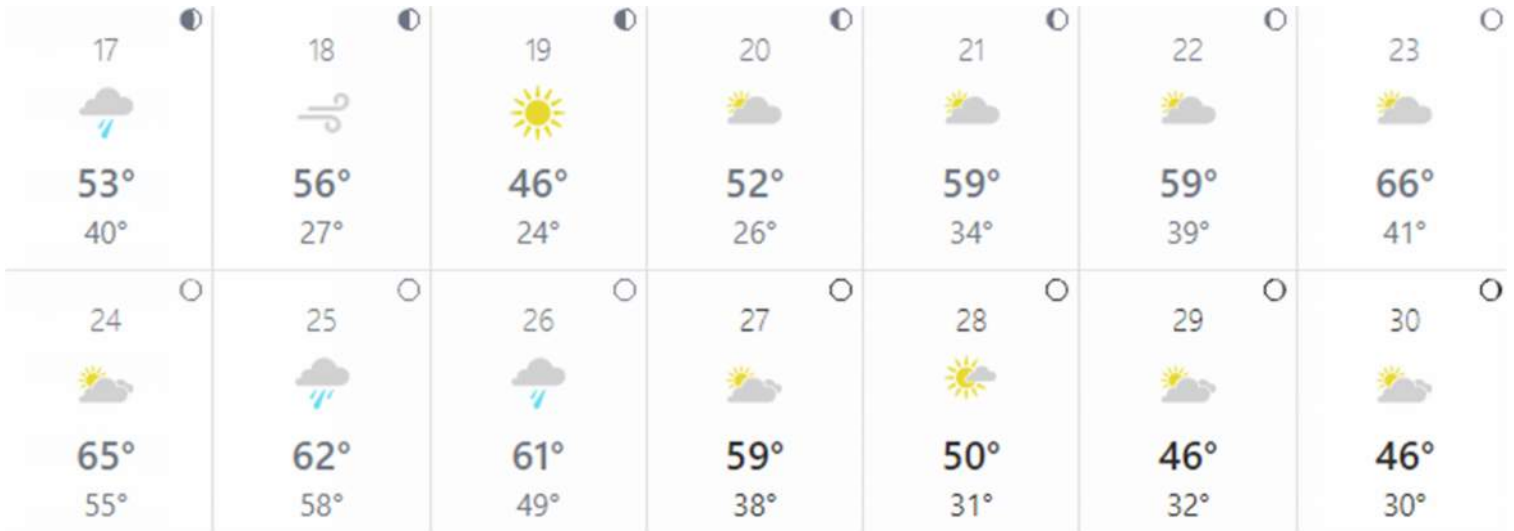

## MANPOWER

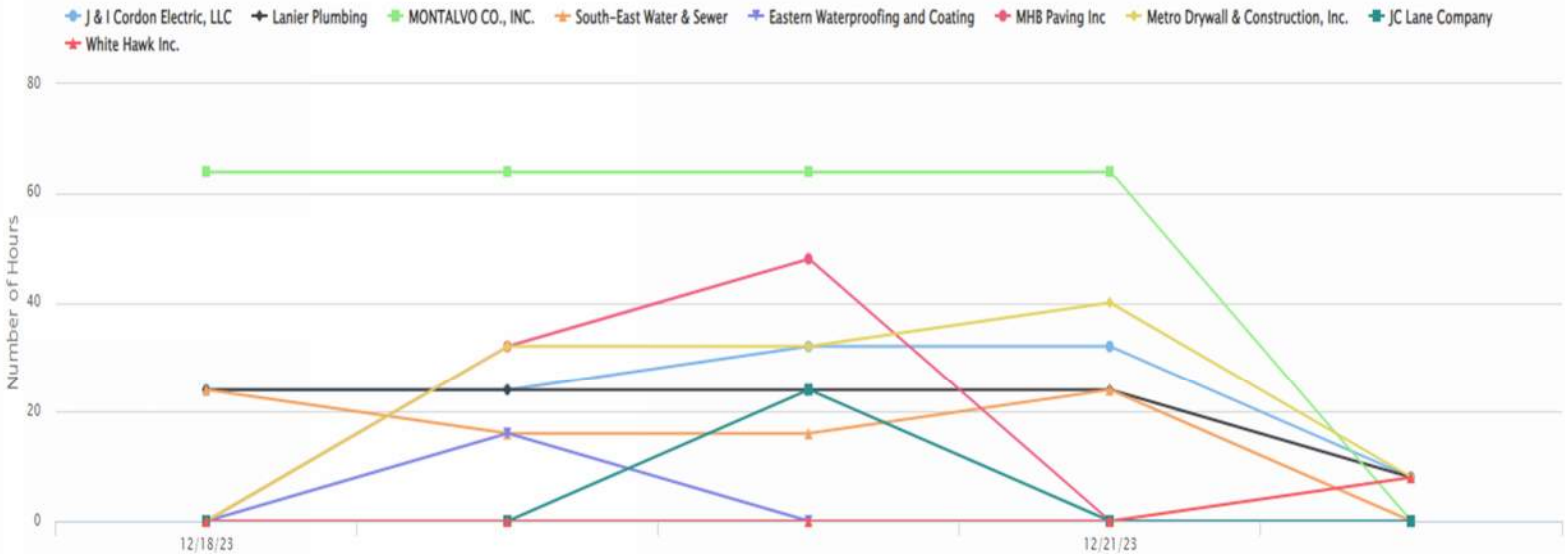

## SAFETY REPORT

- Days without an accident: 180
- Days without lost time: 180

## MILESTONE TRACKING

- Construction Start: April 10, 2023
- Current Contract Completion Date: June 10, 2024
