

CURRENT CONSTRUCTION ACTIVITIES

LAST WEEK

- Began Installing Glass in all Door Frames and Lites
- Began Installing Screen Wall Blocking
- Began Laying Permeable Pavers at Mt Vernon Entrance
- Continued Mudding on First and Second Floor
- Began Prepping Spalding Entrance for Curb and Gutter
- Continued Brick Veneer and Cast Stone Installation
- Poured Sidewalks on Mt Vernon Side

THIS WEEK

- Continue Brick Veneer and Cast Stone Installation
- Continue Mudding on First and Second Floor
- Continue Screen Wall Installation
- Continue Prepping Spalding Entrance for Curb and Gutter
- Continue Laying Permeable Pavers at Mt Vernon Parking


 JOBSITE PHOTOS



Began Laying Permeable Pavers at Mt Vernon Entrance




Began Screen Wall Blocking

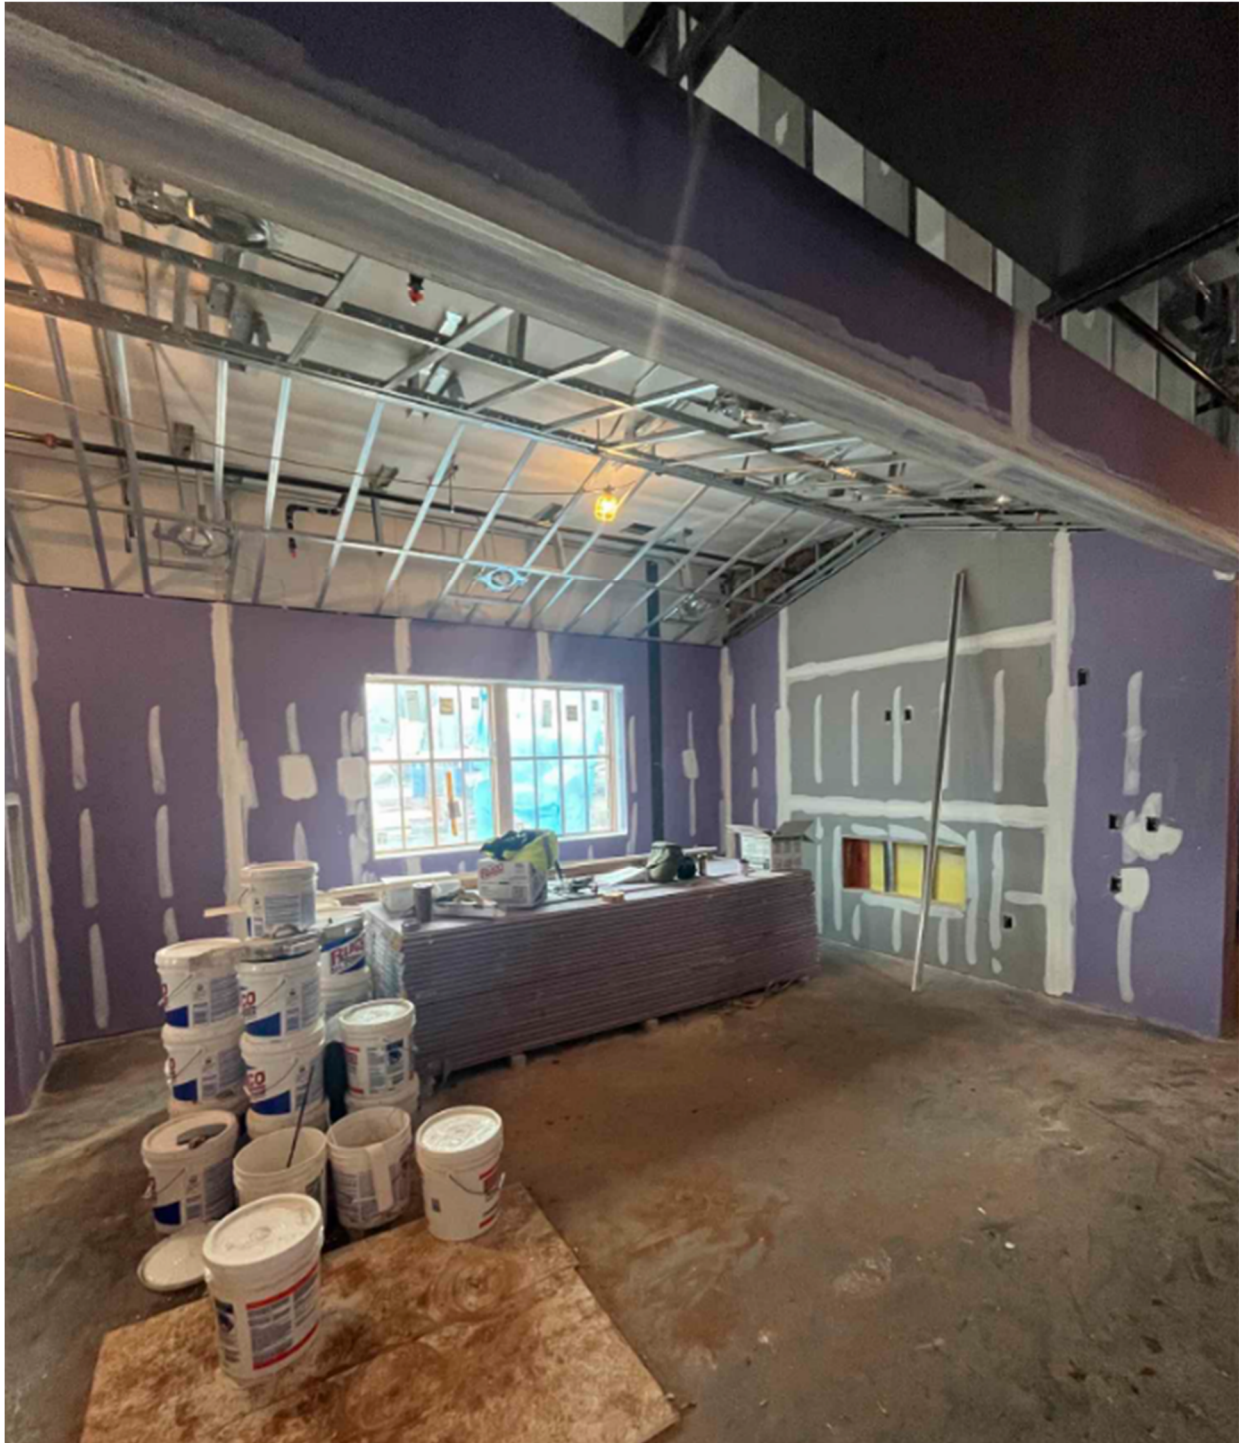

Continued Mudding on First and Second Floor


WEATHER

Weather delays last week: 0

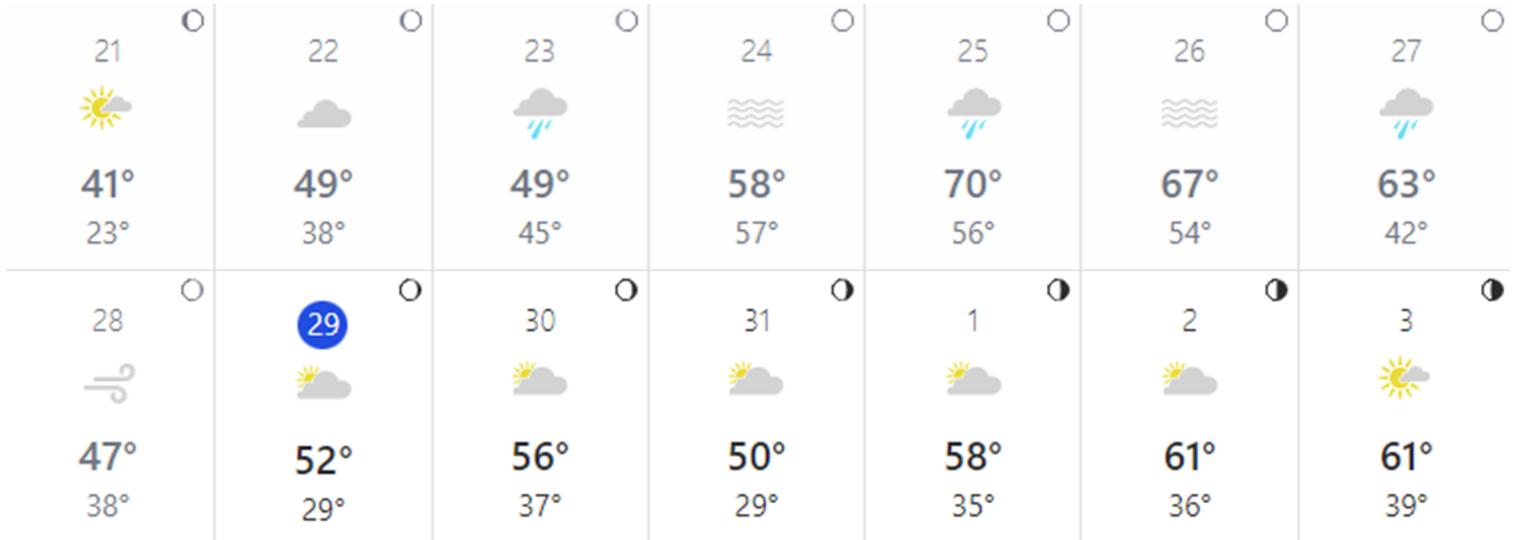

MANPOWER

Clearvue Glass & Mirror Compnay
 J & I Cordon Electric, LLC
 MONTALVO CO., INC.
 Paverstone Construction
 Performance Construction Services, LLC
 South-East Water & Sewer
 Lanier Plumbing
 Davis Engineering & Surveying, LLC
 JC Lane Company
 Metro Drywall & Construction, Inc.
 Southern Painting LLC

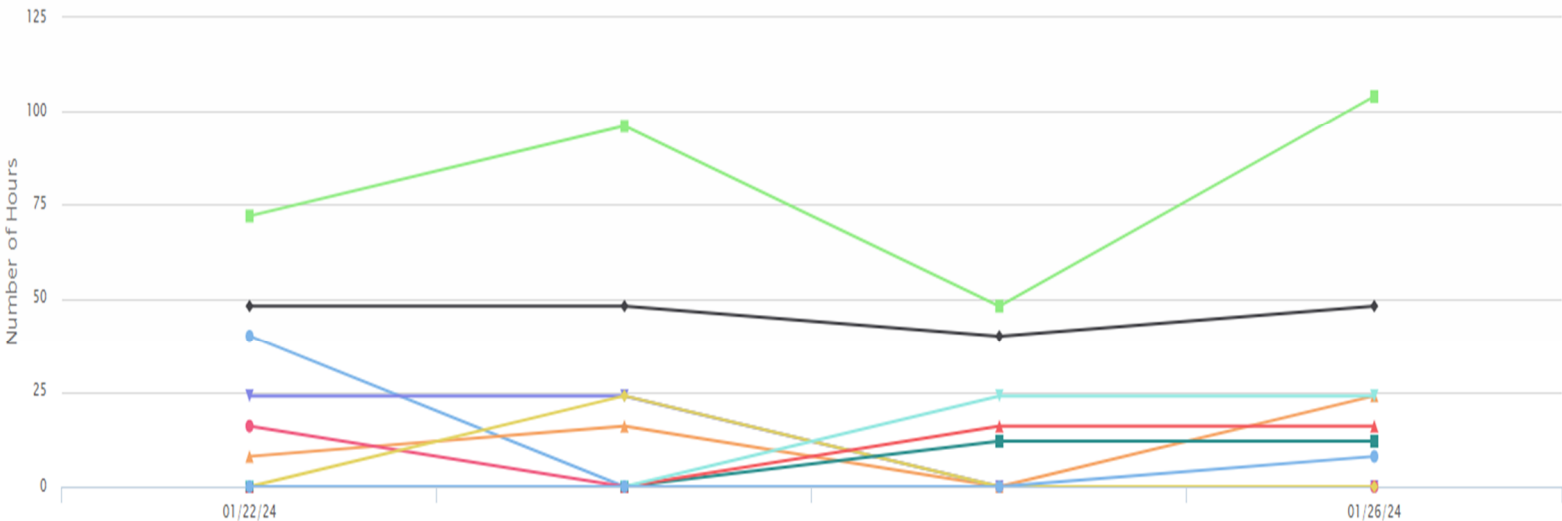

SAFETY REPORT

- Days without an accident: 205
- Days without lost time: 205

MILESTONE TRACKING

- Construction Start: April 10, 2023
- Current Contract Completion Date: June 10, 2024
