

+ CURRENT CONSTRUCTION ACTIVITIES

LAST WEEK

- Began Painting on First Floor
- Began Priming for Paint on Second Floor
- Began Installing Brick Veneer and Cast Stone Pillars for Site Fence
- Continued Screen Wall Installation
- Continued Concrete Apron at Spalding Dr and Apparatus Bay
- Continued Brick Veneer and Cast Stone Installation
- Began Acoustical Ceiling Install on First Floor

THIS WEEK

- Continue Primer and Paint
- Continue Site Fence Pillars Installation
- Continue Screen Wall Installation
- Continue Concrete Apron Installation at Spalding Dr and Apparatus Bay
- Continue Installing Acoustical Ceiling on First Floor

 JOBSITE PHOTOS



Continued Screen Wall Installation




Began Installing Brick Veneer and Cast Stone Pillars for Site Fencing



Began Installing Acoustical Ceiling Tile on First Floor


WEATHER

Weather delays last week: 0

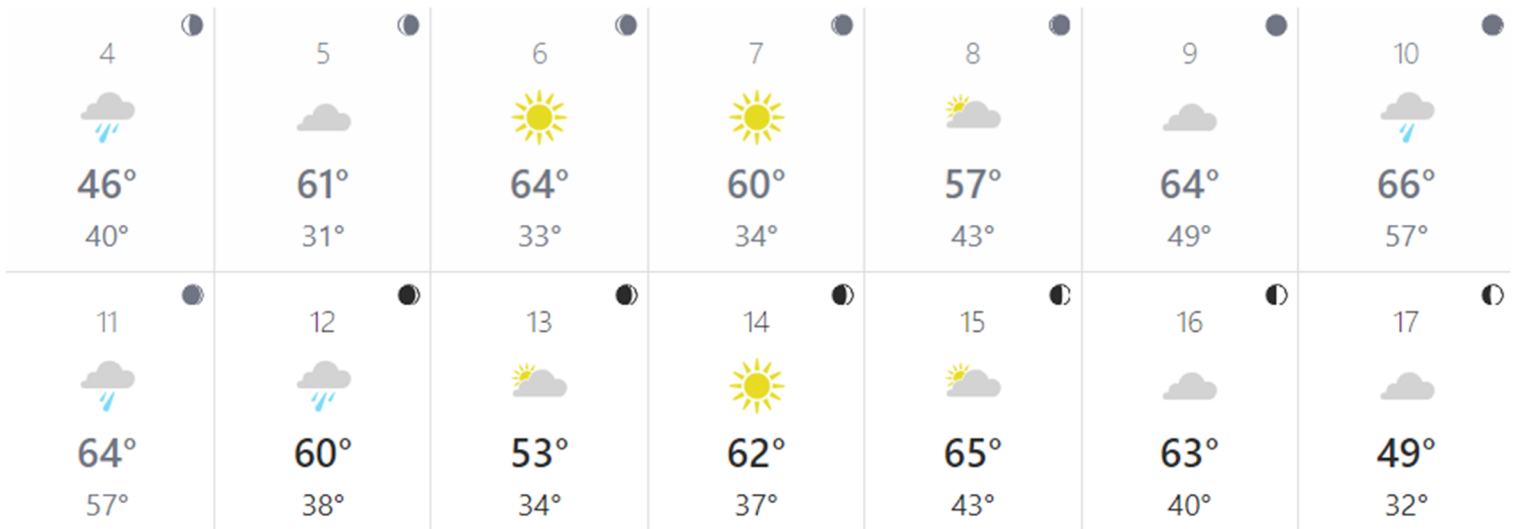

MANPOWER

◆ J & I Cordon Electric, LLC
 ◆ JC Lane Company
 ◆ Lanier Plumbing
 ◆ MONTALVO CO., INC.
 ◆ Metro Drywall & Construction, Inc.
 ◆ Performance Construction Services, LLC
 ◆ Clearvue Glass & Mirror Company

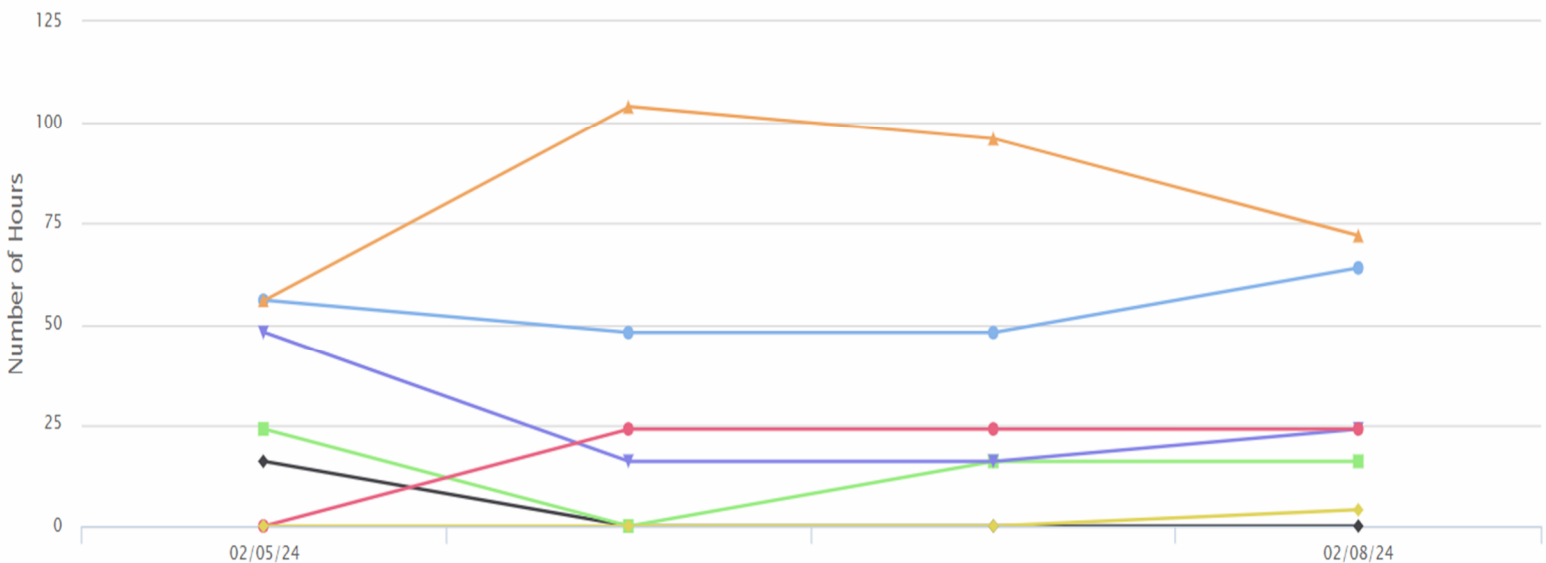

SAFETY REPORT

- Days without an accident: 215
- Days without lost time: 215

MILESTONE TRACKING

- Construction Start: April 10, 2023
- Current Contract Completion Date: June 10, 2024
