

CURRENT CONSTRUCTION ACTIVITIES

LAST WEEK

- Continued Fiber Cement Soffit and Siding Installation
- Continued Light Fixture Installation at The First and Second Levels
- Complete First Coat of Paint at First and Second Levels
- Completed Exterior Paint Color Mock-ups
- Completed Installation of Wall Tile at the Second Floor Restrooms
- Continued Installation of Compressed Air System
- Began Installation of Plumbing Fixtures at the First and Second Floor
- Start-up HVAC units for Interior Finishes Buildout
- Continued Wiring for Apparatus Bay Bi-fold Door Start-up
- Completed Kitchen Hood and Grease Duct at Kitchen
- Set OCS Permanent Structure at Retention Pond

THIS WEEK

- Complete Fiber Cement Soffit and Siding Installation
- Continue Light Fixture Installation at The First and Second Levels
- Complete First Coat of Paint at First and Second Levels
- Complete Installation of Wall Tile at the Second Floor Restrooms
- Continue Brick Veneer at Kitchen Chimney
- Complete Cleaning Exterior Brick Veneer and Cast Stone
- Continue Installation of Plumbing Fixtures
- Begin Prepping for Installation of Exterior Paint

+ JOBSITE PHOTOS



Set OCS Structure at Retention Pond




Continued Prep for Bi-Fold Door Start-up at Apparatus Bay



Continued Hardie Shingle Siding at the TPO Roof


WEATHER

Weather delays last week: 0

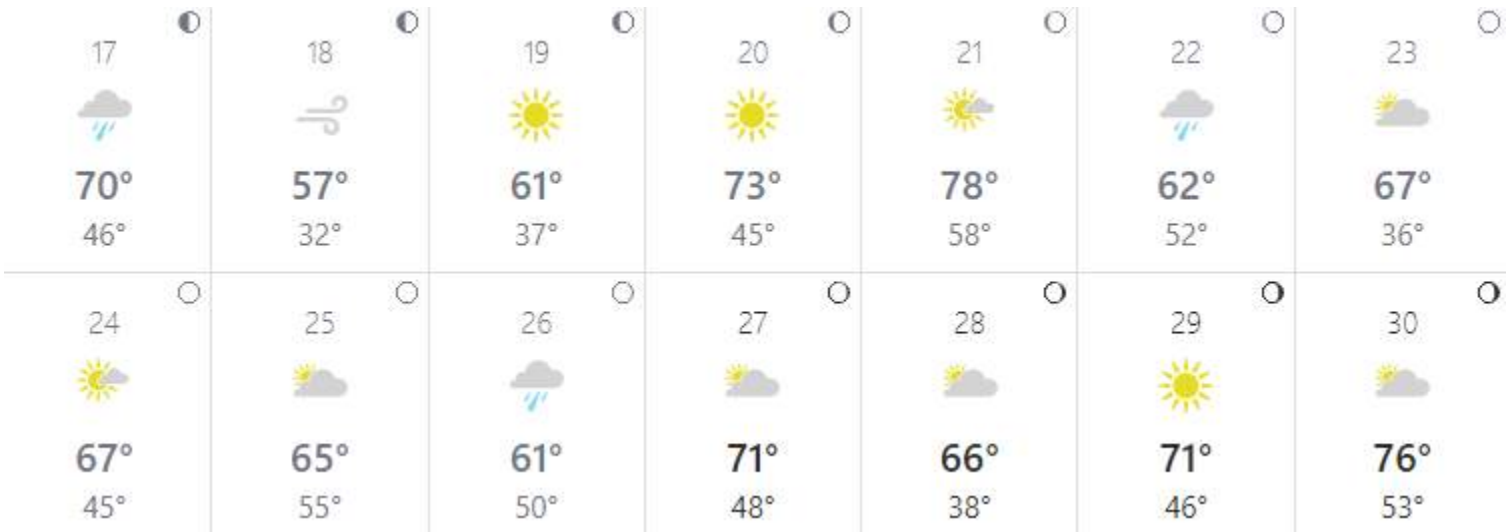

MANPOWER

MANPOWER GRAPH

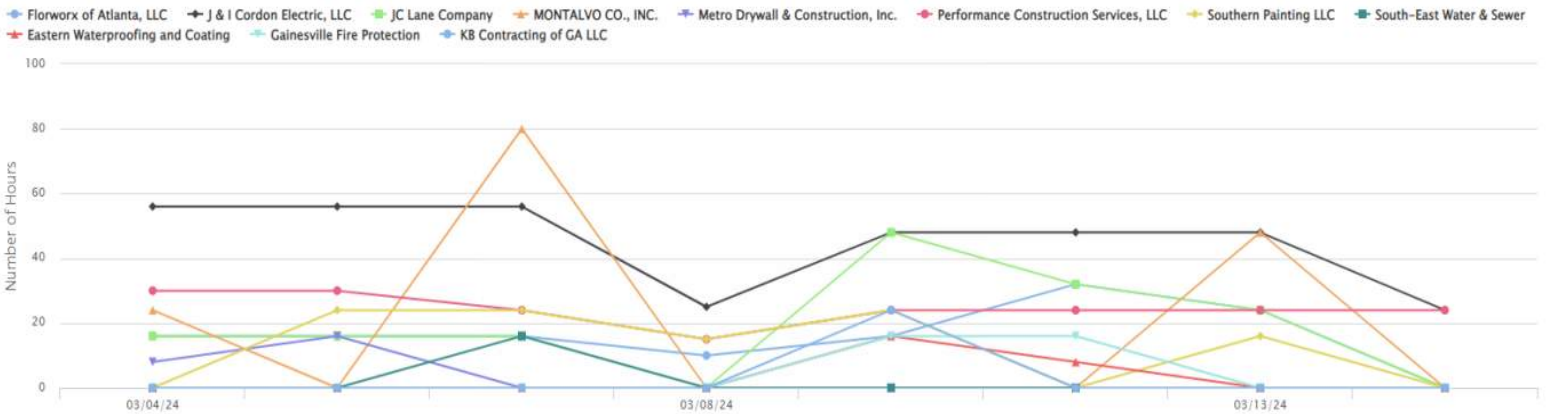

SAFETY REPORT

- Days without an accident: 250
- Days without lost time: 250

MILESTONE TRACKING

- Construction Start: April 10, 2023
- Current Contract Completion Date: June 10, 2024
