

+ CURRENT CONSTRUCTION ACTIVITIES

LAST WEEK - WEEK ENDING 01/13/2023

- Completed concrete pour in the back parking lot up to the dumpster pad.
- Building insulation was installed.
- GAB laid and compacted in the front of the building.
- Fans installed in shop area.
- Drywall hung in office.
- Began installing Simple Saver throughout the building.
- Began overhead doors install.


THIS WEEK - WEEK ENDING 01/20/2024

- Building insulation installed.
- Electricians to continue to pull wire.
- Drywall finishers will begin.
- Glass for windows will be delivered and installed.
- Begin installation of air handler, louvers, and exhaust fans.
- Doors will be delivered and installed.
- Metal paneling in the shop area will be installed.

 JOBSITE PHOTOS



Building Insulation Was Installed

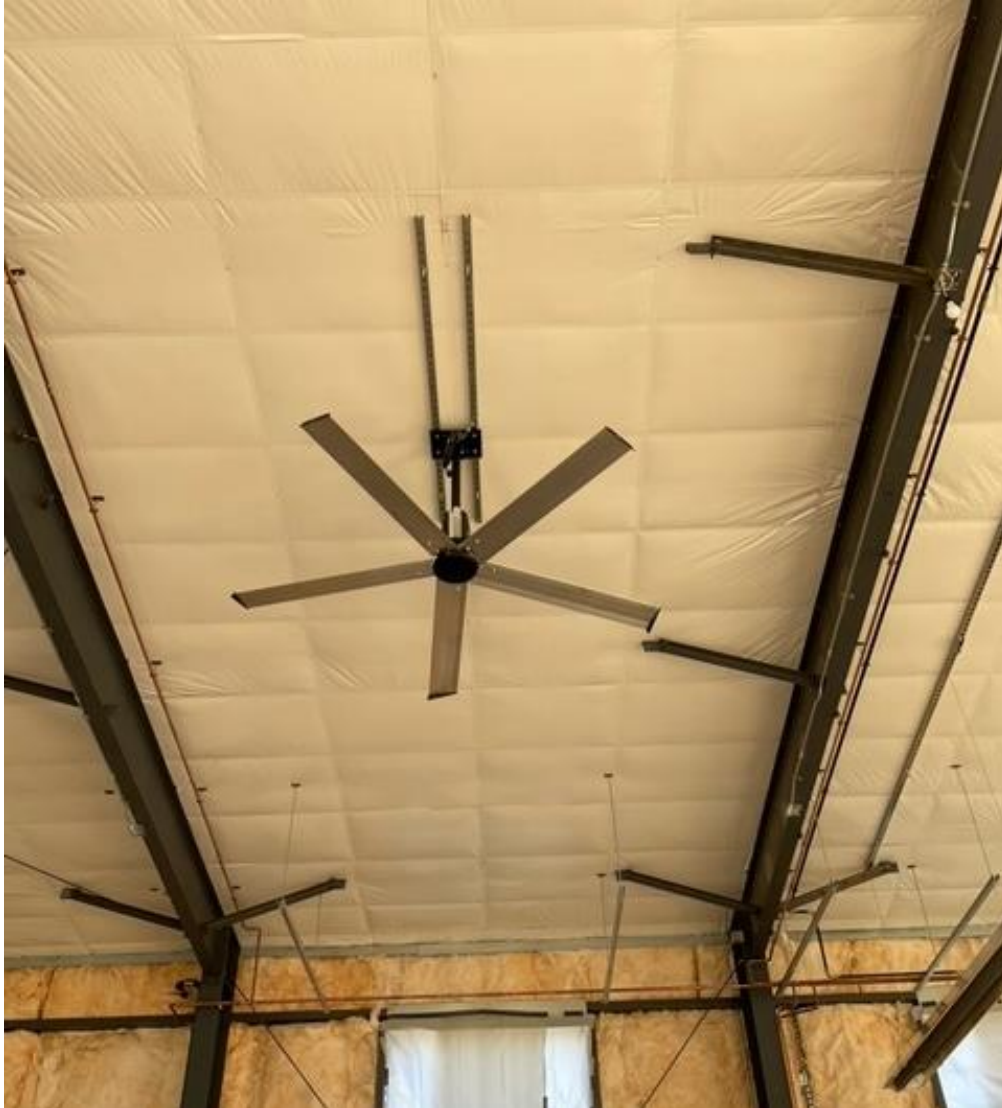

Fans Installed In Shop Area



Drywall Was Hung In The Office Area



Began Installing Simple Saver



GAB Was Laid And Compacted In Front Of The Building

















Poured The Back Parking Lot



Overhead Doors Are Being Installed

WEATHER

Weather delays last week: 1

7  48° 29°	8  50° 37°	9  53° 35°	10  49° 28°	11  61° 37°	12  46° 32°	13  44° 26°
14  56° 37°	15  60° 33°	16  31° 13°	17  38° 19°	18  48° 36°	19  42° 15°	20  34° 14°

- Total Weather Delays: 3

SAFETY REPORT

- Days without an accident: 114
- Days without lost time: 114

MILESTONE TRACKING

- Construction Start: August 21, 2023
- Current Contract Completion Date: March 19, 2024
