

CURRENT CONSTRUCTION ACTIVITIES

LAST WEEK

- Continued Fiber Cement Soffit and Siding Installation
- Continued Light Fixture Installation at The First and Second Levels
- Continued First Coat of Paint at the Second Floor
- Continued Installation of Floor and Wall Tile at the Second Floor Restrooms
- Completed Pour of Sidewalks at Spalding Dr
- Continued Installation of Compressed Air System
- Completed Cleaning Exterior Brick Veneer and Cast Stone
- Continued LV Wiring for Mini-Split Units at First and Second Levels

THIS WEEK

- Complete Fiber Cement Soffit and Siding Installation
- Continue Light Fixture Installation at The First and Second Levels
- Complete First Coat of Paint at First and Second Levels
- Complete Exterior Paint Color Mock-ups
- Complete Installation of Wall Tile at the Second Floor Restrooms
- Continue Installation of Compressed Air System
- Complete Cleaning Exterior Brick Veneer and Cast Stone
- Begin Installation of Plumbing Fixtures at the First Floor
- Start-up HVAC units for Interior Finishes Buildout
- Complete Wiring for Apparatus Bay Bi-fold Door Start-up
- Apparatus Bay Bi-fold Door Start-up

+ JOBSITE PHOTOS



Continued Overhead Paint and Device Wiring at the First Floor Gym



Completed Installation of Sidewalk at Spalding Drive



Continued Wiring for Mini-Split Units at the Second Level


WEATHER

Weather delays last week: 0



MANPOWER

MANPOWER GRAPH

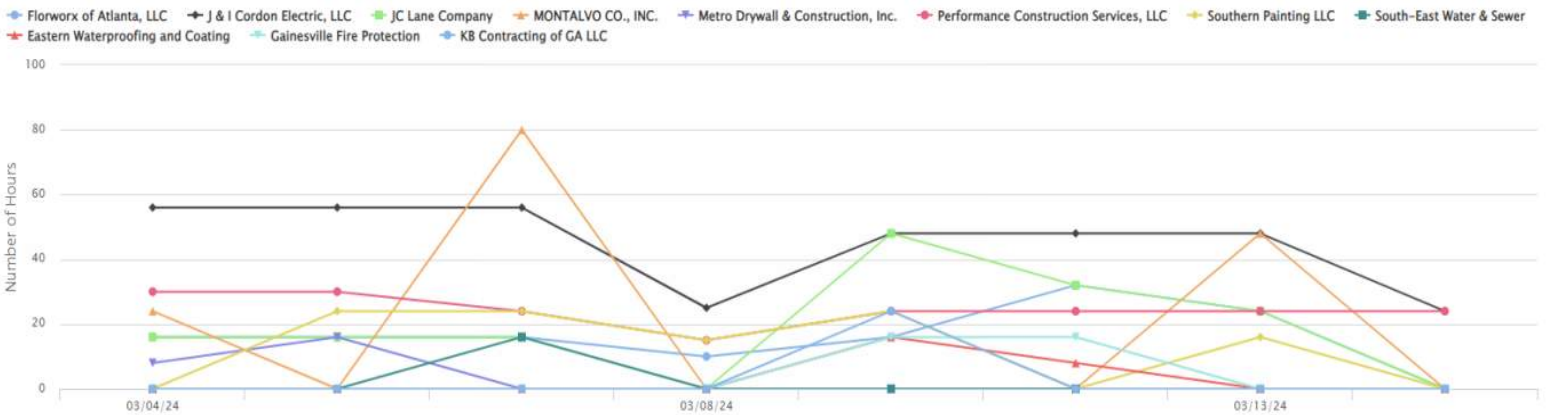

SAFETY REPORT

- Days without an accident: 240
- Days without lost time: 240

MILESTONE TRACKING

- Construction Start: April 10, 2023
- Current Contract Completion Date: June 10, 2024
