

CURRENT CONSTRUCTION ACTIVITIES

LAST WEEK - WEEK ENDING 02/15/2025

2nd Floor:

- Architectural Punch Walk
- Terminating Data Cable in the IT Room
- T&B

1st Floor:

- Flooring
- Millwork at Courtroom
- Restroom Partitions
- Paint Touch-Up
- Toilet Partitions

Basement:

- Pulling Data & Fire Alarm Cable
- Service Elevator Final Inspection

Exterior:

- Prepping & Laying Pavers at the Plaza
- Site Fencing
- Spreading Topsoil
- Spreading GAB
- Binder

THIS WEEK - WEEK ENDING 02/22/2025

2nd Floor:

- Architectural Punch Work
- Terminating Data Cable in the IT Room

1st Floor:

- Flooring
- Millwork at Courtroom
- Paint Touch-Up
- Faux Wood Metal Panel
- Doors & Hardware


Basement:

- VESDA at Data Center

Exterior:

- Prepping & Laying Pavers at the Plaza
- Site Fencing
- Generator Start-Up

 JOBSITE PHOTOS

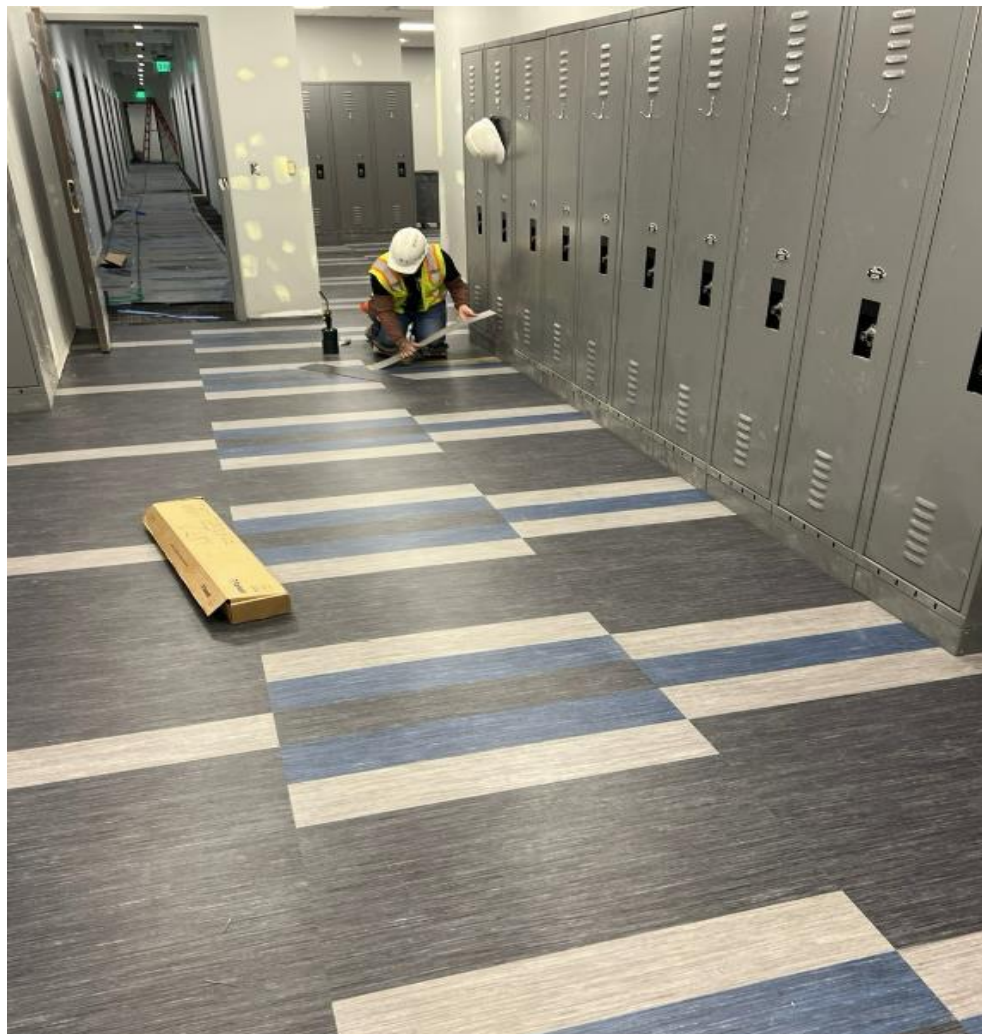

LVT at Locker Rooms



Faux Wood Panel

















Pavers at Plaza



Millwork at Courtroom

 WEATHER

Weather delays this week: 1

9  72° 47°	10  62° 42°	11  44° 35°	12  40° 38°	13  60° 26°	14  56° 39°	15  45° 43°
16  56° 28°	17  51° 28°	18  -- 37°	19  43° 24°	20  35° 19°	21  45° 23°	22  52° 29°

- Total Weather Delays: 49

SAFETY REPORT

- Days without an accident: 390
- Days without lost time: 390

MILESTONE TRACKING

- Construction Start: August 21, 2023
- Current Contract Completion Date: Mar 14, 2025
