

CURRENT CONSTRUCTION ACTIVITIES

LAST WEEK - WEEK ENDING 11/25/2023

- Electrical overhead rough-in on level 3.
- Continue fireproofing on level 2.
- MEP overhead rough-in on levels 1 & 2.
- Continue joist augmentation on level 1.
- Continue slab demolition on the basement.
- Continue exterior demo of brick/glass/lintel/kicker.
- Continue asphalt demolition and retaining wall demolition.

THIS WEEK - WEEK ENDING 12/02/2023

- Continue electrical overhead rough-in on level 3.
- Begin mechanical PIU/VAV rough-in on level 3.
- Begin mechanical overhead rough-in on level 2.
- Continue joist augmentation on level 1.
- Begin fireproofing on level 1.
- Continue slab demolition on the basement.
- Begin joist augmentation on the basement.
- Begin stair 1 steel installation on the roof.
- Continue exterior demo brick/glass/lintel/kicker.
- Begin installing storm line "A".
- Begin grading at sally port.

 JOBSITE PHOTOS



Continue exterior demo of brick/glass/lintel/kicker - West Face




Continue Fireproofing On Level 1




Continue Mecanical PIU/VAV Rough-In



Continue exterior demo of brick/glass/lintel/kicker - North Face

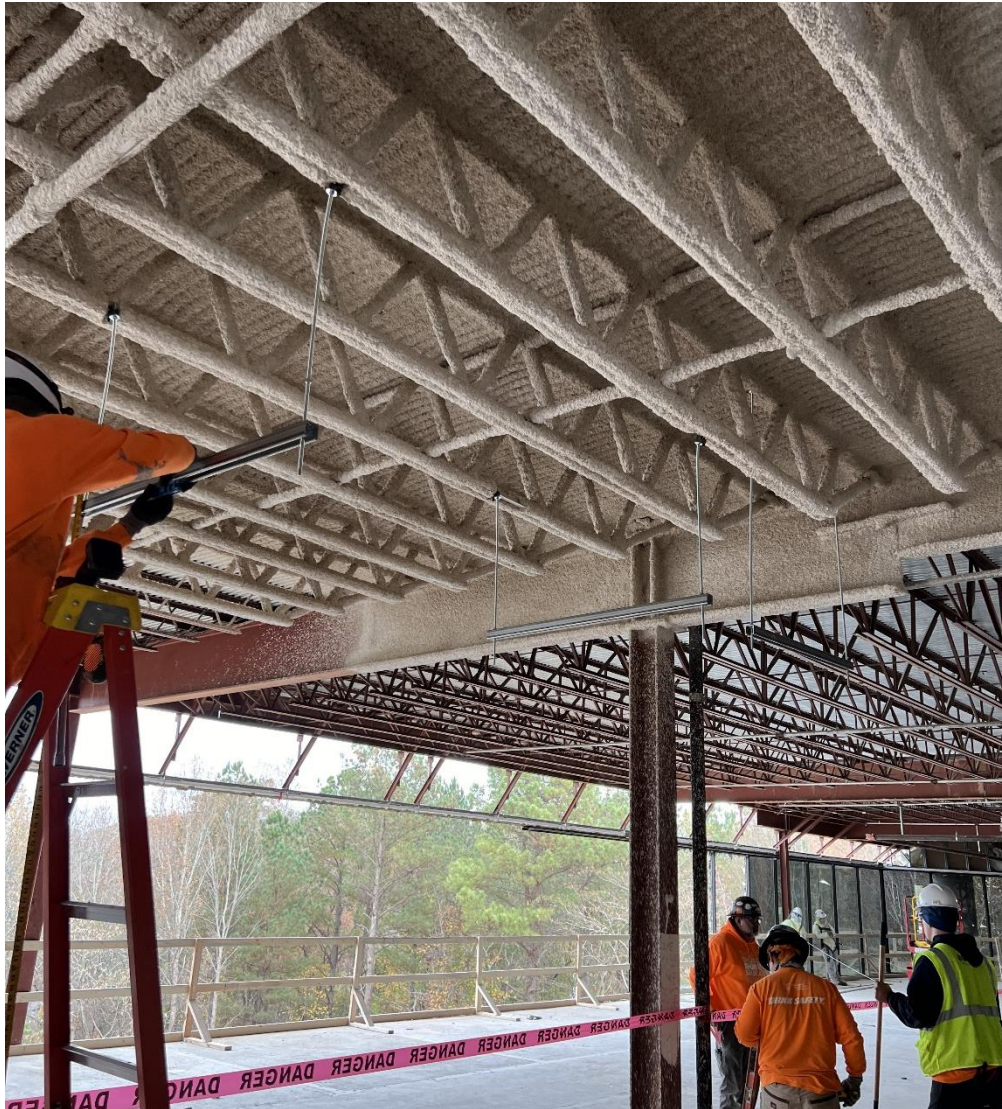

Mechanical Overhead Rough-in On Level 2

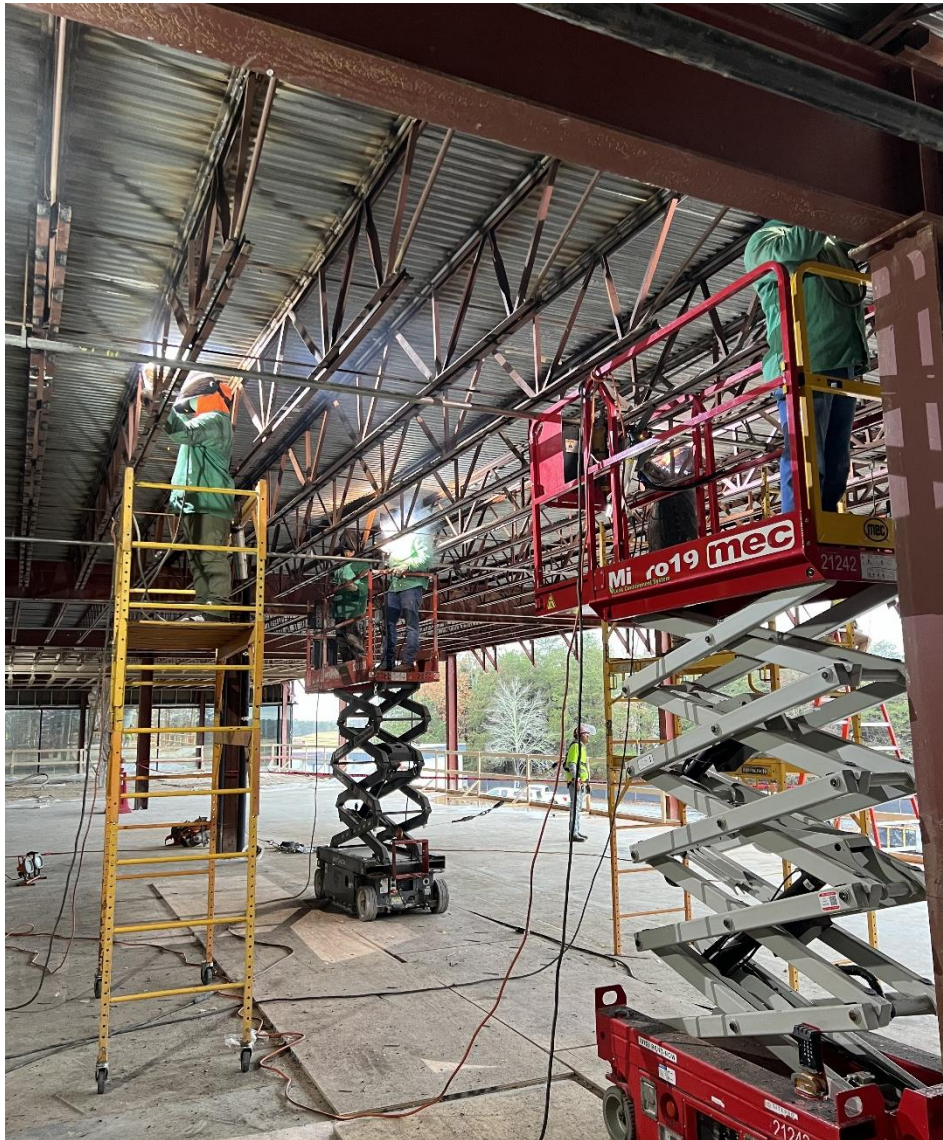

Continue joist augmentation on level 1



Continue Exterior Demo of Brick/Glass/Lintel/Kicker - North Face



Begin Demo & Grading at Retaining Wall

















Begin Grading At Sally Port



Continue Demolition Of The Basement Slab

 WEATHER

Weather delays last week: 0

| | | | | | | |
|---|---|---|---|--|---|---|
| 19  67° 51° | 20  60° 50° | 21  66° 52° | 22  53° 37° | 23  58° 41° | 24  63° 41° | 25  56° 43° |
| 26  47° 39° | 27  49° 34° | 28  50° 26° | 29  53° 32° | 30  61° 44° | 1  54° 51° | 2  61° 56° |

SAFETY REPORT

- Days without an accident: 57
- Days without lost time: 57

MILESTONE TRACKING

- Construction Start: August 21, 2023
- Current Contract Completion Date: Mar 14, 2025
