

CURRENT CONSTRUCTION ACTIVITIES


THIS WEEK - WEEK ENDING 09/23/2023

- Demo existing conditions on levels 3 and 4
- Exporting and recycling of demolished materials
- Connecting temporary lights
- Connecting temporary power
- MEP make-safe

NEXT WEEK - WEEK ENDING 9/30/2023

- Continued demolition of existing conditions
- Continued export and recycling of demolished materials

 JOBSITE PHOTOS

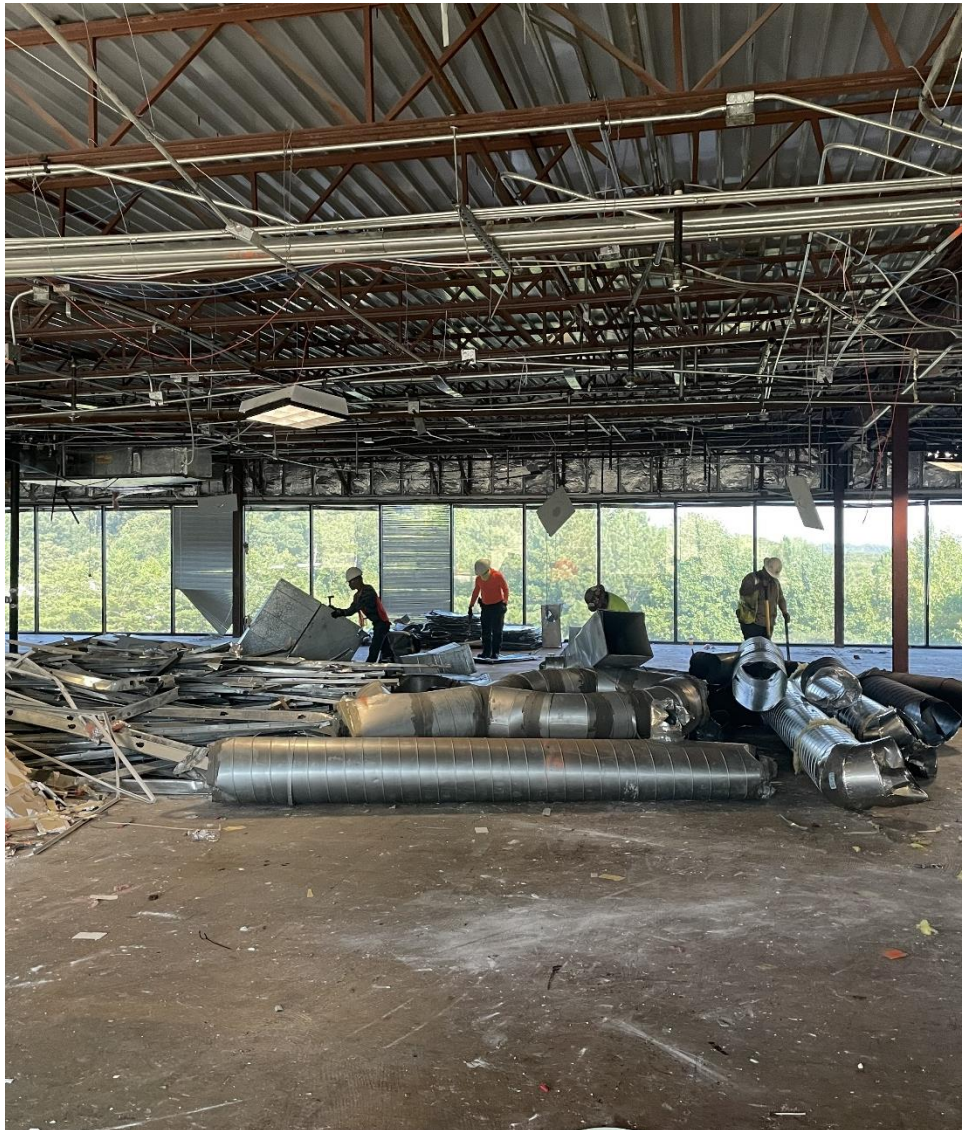

Demolishing Existing Conditions



Connecting Temporary Light and Power



Demolishing Existing Conditions



Demolishing Existing Conditions



Exporting Demolished Materials

+ WEATHER

Weather delays last week: 0

10 84° 66°	11 89° 68°	12 87° 69°	13 85° 67°	14 78° 67°	15 74° 63°	16 71° 63°
17 80° 56°	18 78° 55°	19 80° 59°	20 80° 62°	21 79° 60°	22 78° 60°	23 79° 60°

+ MANPOWER

- TBD

SAFETY REPORT

- Days without an accident: 17
- Days without lost time: 17

MILESTONE TRACKING

- Construction Start: August 21, 2023
- Current Contract Completion Date: May 17, 2024
